

Driscoll School - Gantt Chart


Plans: Multiple Plans Selected

Start Date: Monday January 23 2023

Roles: Multiple Roles Selected

End Date: Sunday February 19 2023

Locations: Multiple Locations Selected (Not including Location-less tickets)

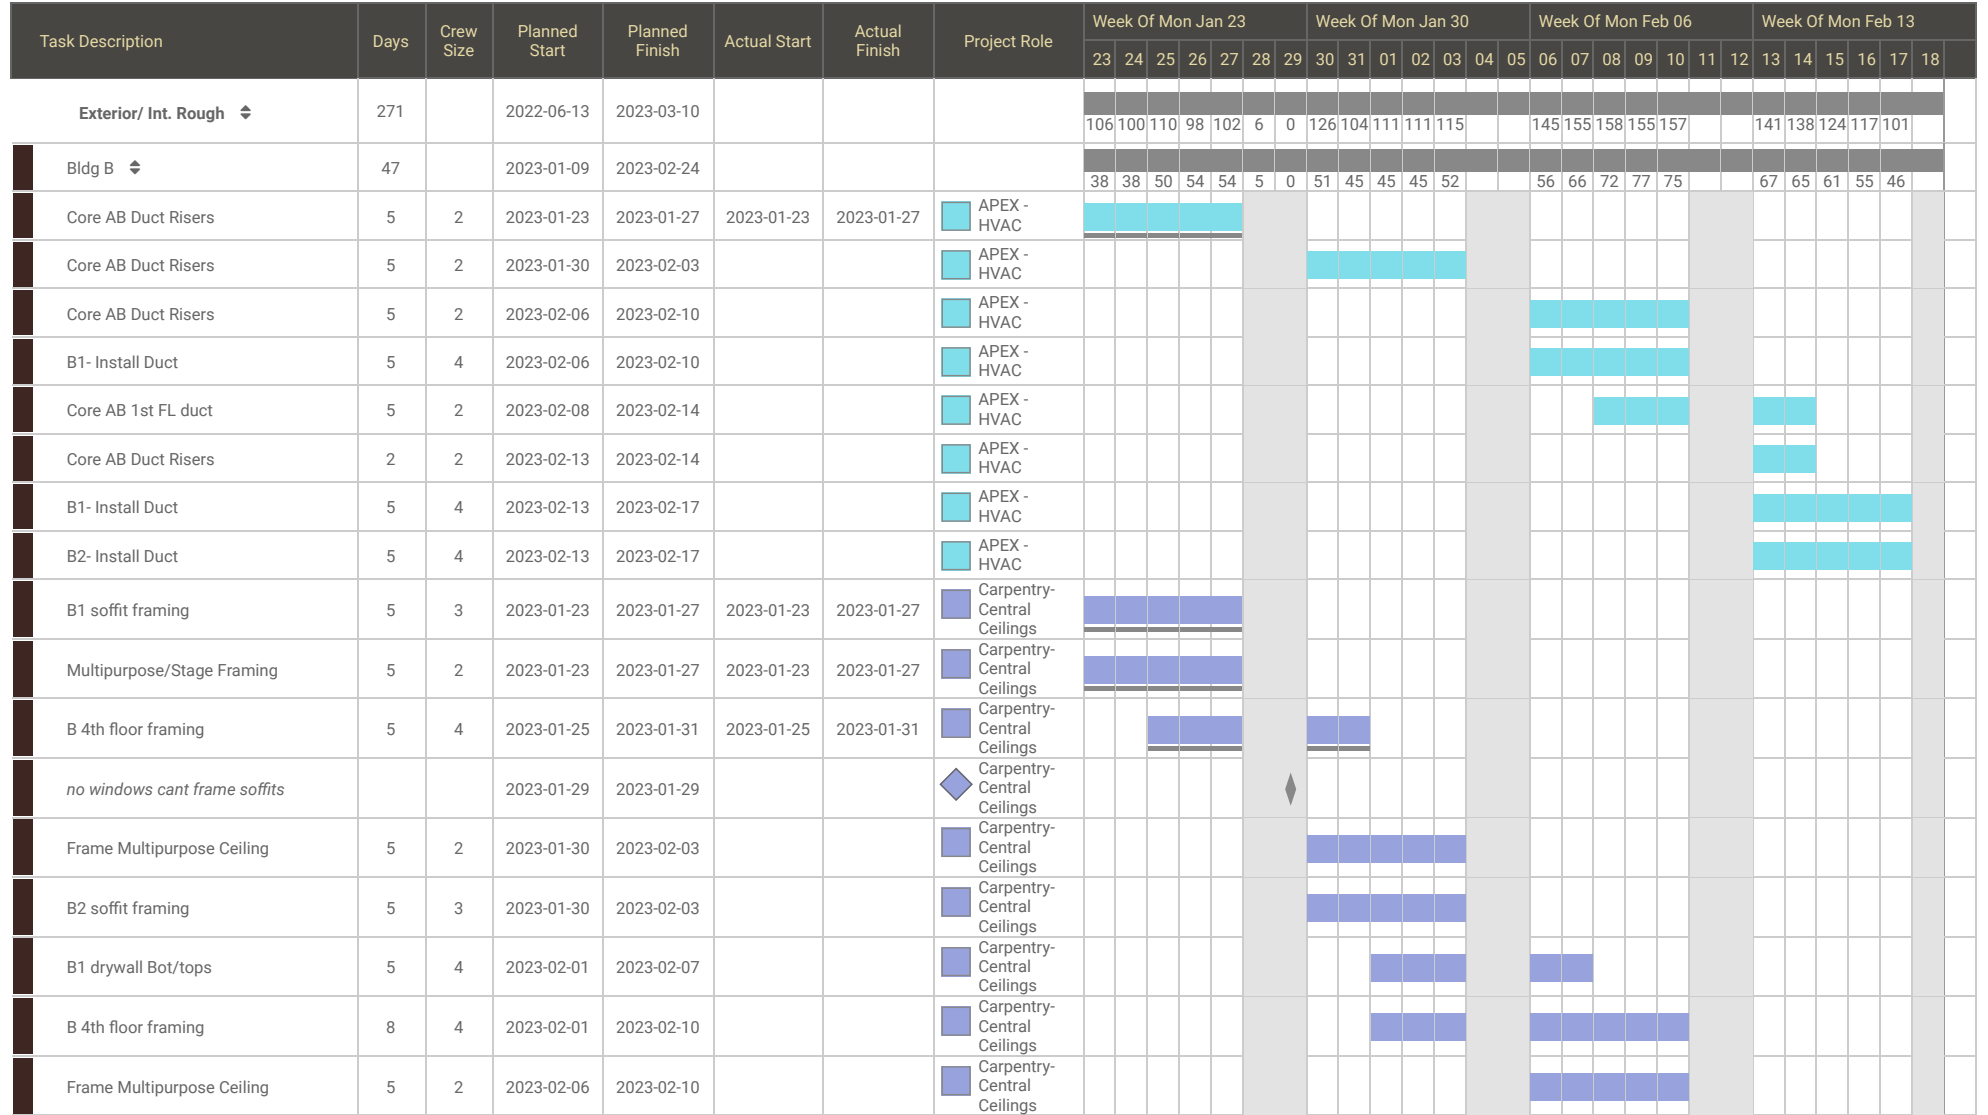

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13						
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	
B2 drywall tops	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																												
B3 soffit framing	5	3	2023-02-06	2023-02-10			Carpentry-Central Ceilings																												
B4 soffit framing	5	3	2023-02-06	2023-02-10			Carpentry-Central Ceilings																												
B1 drywall Bot/tops	5	4	2023-02-08	2023-02-14			Carpentry-Central Ceilings																												
B2 drywall Bot/tops	5	4	2023-02-09	2023-02-15			Carpentry-Central Ceilings																												
Frame Multipurpose Ceiling	5	2	2023-02-13	2023-02-17			Carpentry-Central Ceilings																												
B3 drywall tops	5	4	2023-02-13	2023-02-17			Carpentry-Central Ceilings																												
Layout Core AB FL-1	2	2	2023-02-15	2023-02-16			Carpentry-Central Ceilings																												
Close AB Shaft- FL 2	5	2	2023-02-15	2023-02-21			Carpentry-Central Ceilings																												
B2 drywall Bot/tops	5	4	2023-02-16	2023-02-22			Carpentry-Central Ceilings																												
Frame Walls Core AB FL-1	4	2	2023-02-17	2023-02-22			Carpentry-Central Ceilings																												
Prep/Pour Stair 4 Concrete	4	4	2023-02-07	2023-02-10			Concrete-Marguerite																												
B1- In-wall Elec Rough in	9	3	2023-01-17	2023-01-27	2023-01-17	2023-01-27	Electrical-Griffin																												
B1 - O.H. Elec Rough	10	2	2023-01-19	2023-02-01	2023-01-19	2023-02-01	Electrical-Griffin																												
B2- In-wall Elec Rough in	10	4	2023-01-23	2023-02-03			Electrical-Griffin																												
B2- O.H. Elec Rough	10	2	2023-01-26	2023-02-08			Electrical-Griffin																												
Level-3- In-wall Elec Rough in	10	3	2023-02-06	2023-02-17			Electrical-Griffin																												
Auditorium In Wall Rough	12	2	2023-02-07	2023-02-22			Electrical-Griffin																												
Auditorium OH Rough	10	2	2023-02-13	2023-02-24			Electrical-Griffin																												
Auditorium Theater Lighting Control Rough	10	2	2023-02-13	2023-02-24			Electrical-Griffin																												
Level-3- O.H. Elec Rough	10	2	2023-02-13	2023-02-24			Electrical-Griffin																												
Level-4- In-wall Elec Rough in	10	4	2023-02-13	2023-02-24			Electrical-Griffin																												
Auditorium In wall Inspection			2023-01-31	2023-01-31			GC - Gilbane																												
B2 In- Wall Inspection			2023-02-08	2023-02-08			GC - Gilbane																												
B3 In- Wall Inspection			2023-02-17	2023-02-17			GC - Gilbane																												
Stair 4 Combo Riser	3	2	2023-02-13	2023-02-15			JCI- Fire Protection																												

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13						
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	
Brick Install B North	5	10	2023-01-19	2023-01-25	2023-01-19	2023-01-25	Masonry-Fernandes	█	█	█	█	█																							
Brick Install B North	7	10	2023-01-26	2023-02-03			Masonry-Fernandes																												
Complete on Hydromobile B North	2	0	2023-02-06	2023-02-07			Masonry-Fernandes																												
Brick Install B North	5	10	2023-02-06	2023-02-10			Masonry-Fernandes																												
Layout and Flashing B West	1	4	2023-02-08	2023-02-08			Masonry-Fernandes																												
Brick Install B West	5	5	2023-02-09	2023-02-15			Masonry-Fernandes																												
Wash Brick North	3	2	2023-02-09	2023-02-13			Masonry-Fernandes																												
Brick Install B West	5	5	2023-02-16	2023-02-22			Masonry-Fernandes																												
Stair 4 Install	8	4	2023-01-25	2023-02-03			Misc Metal-United																												
Inwall Plmb (San/Waste/Water) - Level 1 (1 of 2)	7	2	2023-01-19	2023-01-27	2023-01-19	2023-01-27	Plumbing-PJ Kennedy	█	█	█	█	█	█																						
B Riser #1	5	2	2023-01-26	2023-02-01	2023-01-26	2023-02-01	Plumbing-PJ Kennedy																												
B Riser #1	5	2	2023-02-02	2023-02-08			Plumbing-PJ Kennedy																												
B Riser #2	5	2	2023-02-02	2023-02-08			Plumbing-PJ Kennedy																												
B1 Inspection			2023-02-07	2023-02-07			Plumbing-PJ Kennedy																												
B Riser #2	5	2	2023-02-09	2023-02-15			Plumbing-PJ Kennedy																												
B Riser #3	5	2	2023-02-09	2023-02-15			Plumbing-PJ Kennedy																												
B Riser #3	5	2	2023-02-16	2023-02-22			Plumbing-PJ Kennedy																												
B Riser #4	5	2	2023-02-16	2023-02-22			Plumbing-PJ Kennedy																												
Install Main Roof	16	6	2023-01-09	2023-01-30	2023-01-09	2023-01-30	Roofing- JD Rivet	█	█	█	█	█	█	█	█	█	█	█	█	█	█														
Install Roof At Stair 4	1	5	2023-01-28	2023-01-28	2023-01-28	2023-01-28	Roofing- JD Rivet																												
B4 roof	4	7	2023-02-03	2023-02-08			Roofing- JD Rivet																												
B3 roof	6	7	2023-02-09	2023-02-16			Roofing- JD Rivet																												
Release #8 Frames Install	12	4	2023-01-16	2023-01-31			Storefront/Metal Panels-Salem	█	█	█	█	█	█	█	█	█	█	█	█	█	█														
Release #6 Frames Install	5	4	2023-01-25	2023-01-31	2023-01-25	2023-01-31	Storefront/Metal Panels-Salem																												
Release #6A Glazing Install	5	2	2023-01-30	2023-02-03			Storefront/Metal Panels-Salem																												
Release #6 Frames Install	7	4	2023-02-01	2023-02-09			Storefront/Metal Panels-Salem																												

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23					Week Of Mon Jan 30					Week Of Mon Feb 06					Week Of Mon Feb 13											
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18
Release #8 Glazing Install	7	4	2023-02-07	2023-02-15			Storefront/ Metal Panels- Salem																											
Release #6B Glazing Install	5	2	2023-02-10	2023-02-16			Storefront/ Metal Panels- Salem																											
Bldg A ↕	50		2023-01-13	2023-03-03				49	45	44	35	37			59	48	50	49	46			68	68	65	62	67			53	50	43	43	40	
A building 3rd Ductwork	7	3	2023-01-17	2023-01-23	2023-01-17	2023-01-25	APEX - HVAC																											
A building 4th Hangers	5	2	2023-01-23	2023-01-27	2023-01-23	2023-01-27	APEX - HVAC																											
A building 4th Ductwork	5	3	2023-01-30	2023-02-03			APEX - HVAC																											
A building 4th Ductwork	5	3	2023-02-06	2023-02-10			APEX - HVAC																											
A-0 Locker Rm Ductwork	5	2	2023-02-06	2023-02-10			APEX - HVAC																											
A building 4th Ductwork	5	3	2023-02-10	2023-02-16			APEX - HVAC																											
L4 Stairs- Frame Walls	7	2	2023-01-16	2023-01-24	2023-01-16	2023-01-24	Carpentry- Central Ceilings																											
L1 Tectum soffit framing	7	2	2023-01-16	2023-01-24	2023-01-16	2023-01-24	Carpentry- Central Ceilings																											
A2- Hang Drywall	5	4	2023-01-17	2023-01-23	2023-01-17	2023-01-23	Carpentry- Central Ceilings																											
L2 Atrium layout	5	2	2023-01-20	2023-01-26	2023-01-20	2023-01-26	Carpentry- Central Ceilings																											
A2- Tape Drywall	5	4	2023-01-23	2023-01-27	2023-01-23	2023-01-30	Carpentry- Central Ceilings																											
A3- Hang Drywall	5	4	2023-01-23	2023-01-27	2023-01-23	2023-01-27	Carpentry- Central Ceilings																											
A4- Hang Drywall	5	4	2023-01-23	2023-01-27	2023-01-23	2023-01-27	Carpentry- Central Ceilings																											
hang fire rated ceilings	6	2	2023-01-23	2023-01-30	2023-01-23	2023-01-30	Carpentry- Central Ceilings																											
Main Stair soffit- FL1	6	1	2023-01-23	2023-01-30	2023-01-23	2023-01-30	Carpentry- Central Ceilings																											
L1 Summer beams and beam wraps	5	2	2023-01-23	2023-01-27	2023-01-23	2023-01-27	Carpentry- Central Ceilings																											
A2- Hang Drywall	2	4	2023-01-24	2023-01-30	2023-01-24	2023-01-25	Carpentry- Central Ceilings																											
L1 Main stair framing	5	2	2023-01-25	2023-01-31	2023-01-25	2023-01-31	Carpentry- Central Ceilings																											
Atrium layout 3rd	5	2	2023-01-27	2023-02-02	2023-01-27	2023-02-02	Carpentry- Central Ceilings																											
Atrium framing 4th walls at EOS	5	2	2023-01-27	2023-02-02	2023-01-27	2023-02-02	Carpentry- Central Ceilings																											
A1 Frame Window Returns	5	1	2023-01-30	2023-02-03			Carpentry- Central Ceilings																											

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13																				
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18															
Kitchen- Hang Drywall	5	2	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
A2- Tape Drywall	5	4	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
A3- Hang Drywall	5	4	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
A3- Tape Drywall	5	4	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
A4- Hang Drywall	5	4	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
L1 Summer beams and beam wraps	5	2	2023-01-30	2023-02-03			Carpentry-Central Ceilings																																										
L1 Main stair framing	5	2	2023-02-01	2023-02-07			Carpentry-Central Ceilings																																										
A1 Hang Drywall- Front offices	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
A2- Tape Drywall	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
A3- Hang Drywall	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
A3- Tape Drywall	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
A4- Tape Drywall	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
A4- Hang Drywall	5	4	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
Top off rated walls	5	2	2023-02-06	2023-02-10			Carpentry-Central Ceilings																																										
L2 Tectum soffit framing	7	2	2023-02-06	2023-02-14			Carpentry-Central Ceilings																																										
Frame & board U/S 4th fl Stair	4	2	2023-02-07	2023-02-10			Carpentry-Central Ceilings																																										
Tank Room Rated Ceiling	8	2	2023-02-09	2023-02-20			Carpentry-Central Ceilings																																										
Atrium frame soffits and walls 3rd	5	2	2023-02-10	2023-02-16			Carpentry-Central Ceilings																																										
A3- Tape Drywall	5	4	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																										
A4- Tape Drywall	5	4	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																										
A4- Hang Drywall	5	4	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																										
A0- drywall bottoms	5	2	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																										
Top 4th Fl stair walls	5	2	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																										

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13						
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	
Frame U/S 3rd Fl Stair	5	2	2023-02-13	2023-02-17			Carpentry-Central Ceilings																												
L1 Boarding soffits	5	2	2023-02-13	2023-02-17			Carpentry-Central Ceilings																												
Spray and fire tape	4	2	2023-02-13	2023-02-16			Carpentry-Central Ceilings																												
Atrium framing 4th soffits and sloped ceilings	5	2	2023-02-17	2023-02-23			Carpentry-Central Ceilings																												
Atrium frame soffits and walls 3rd	5	2	2023-02-17	2023-02-23			Carpentry-Central Ceilings																												
A2 Ceiling Grid- North of corridor	5	2	2023-02-13	2023-02-17			Ceilings-Cheviot																												
Housekeeping Generator Pad	2	3	2023-02-06	2023-02-07			Concrete-Marguerite																												
A0 - Pull Main feeder cables from x-former	3	2	2023-01-30	2023-02-01	2023-01-30	2023-02-01	Electrical-Griffin																												
A0 - Build Electrical Room - Install Mechanical Room Rough Wire	15	2	2023-02-01	2023-02-21			Electrical-Griffin																												
A0 - Build Electrical Room - Install Transformers (hung)	5	2	2023-02-02	2023-02-08			Electrical-Griffin																												
Mechanical Rough	20	1	2023-02-06	2023-03-03			Electrical-Griffin																												
A0 - Build Electrical Room - Install Electrical Room Cable Tray and wire supports - prior to running MC feeders	5	2	2023-02-06	2023-02-10			Electrical-Griffin																												
A0 - Generator Set in place	1	2	2023-02-08	2023-02-08			Electrical-Griffin																												
Rough- Main Stair FL1	5	2	2023-02-08	2023-02-14			Electrical-Griffin																												
A0- Terminate main feeder cables	2	2	2023-02-16	2023-02-17			Electrical-Griffin																												
Main Stair Fireproof	2	2	2023-01-26	2023-01-27			Fireproofing-Ricmor																												
Shut down L4 Main stair- Cut Guardrails	3	1	2023-01-23	2023-01-25	2023-01-23	2023-01-25	GC - Gilbane																												
Build Dancefloors	5	2	2023-01-30	2023-02-03			GC - Gilbane																												
<i>Need Curved Rail Angle</i>			2023-01-30	2023-01-30			GC - Gilbane																												
Cafeteria Summer Beam Rough ins	5	2	2023-02-06	2023-02-10			GC - Gilbane																												
Gen. Room Sprink.	1	2	2023-02-03	2023-02-03			JCI- Fire Protection																												
L3 Stair Sprinkler	1	2	2023-02-06	2023-02-06			JCI- Fire Protection																												
Basement - Mech Rm Piping/Install (9 of 12)	5	5	2023-01-17	2023-01-23	2023-01-17	2023-01-23	Mechanical-PJ Kennedy																												
Basement - Mech Rm Piping/Install (10 of 12)	5	5	2023-01-24	2023-01-30	2023-01-24	2023-01-30	Mechanical-PJ Kennedy																												
Rough Radiation- Auditorium	7	2	2023-01-30	2023-02-07			Mechanical-PJ Kennedy																												

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30					Week Of Mon Feb 06					Week Of Mon Feb 13									
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18
Basement - Mech Rm Piping/Install (11 of 12)	5	5	2023-01-31	2023-02-06			Mechanical-PJ Kennedy																											
Rough Fin Tube- Front offices	3	1	2023-02-06	2023-02-08			Mechanical-PJ Kennedy																											
Basement - Mech Rm Piping/Install (12 of 12)	5	5	2023-02-07	2023-02-13			Mechanical-PJ Kennedy																											
Paint Generator Room Ceiling	1	1	2023-02-02	2023-02-02			Paint- Color Concepts																											
A2- Paint	5	2	2023-02-06	2023-02-10			Paint- Color Concepts																											
A2- Paint	5	2	2023-02-13	2023-02-17			Paint- Color Concepts																											
A3- Paint	5	2	2023-02-13	2023-02-17			Paint- Color Concepts																											
Basement - Water In Wall (1 of 4)	5	3	2023-01-18	2023-01-24	2023-01-18	2023-01-24	Plumbing-PJ Kennedy																											
Basement - In Wall Plumbing/ Showers	5	3	2023-02-06	2023-02-10			Plumbing-PJ Kennedy																											
A2 south roof	3	3	2023-01-30	2023-01-31	2023-01-30	2023-02-01	Roofing- JD Rivet																											
Need Skylights Set			2023-02-13	2023-02-13			Roofing- JD Rivet																											
Phase 5 Priority B South Install SF frames	9	4	2023-01-13	2023-01-25	2023-01-13	2023-01-25	Storefront/ Metal Panels-Salem																											
Phase 5 Priority B South Glazing	6	4	2023-01-23	2023-01-30			Storefront/ Metal Panels-Salem																											
Phase 5 Priority B South Caulk and Spray Foam	5	1	2023-01-26	2023-02-01			Storefront/ Metal Panels-Salem																											
Phase 5 Priority A South Flashing, Girt and insulation	12	3	2023-01-30	2023-02-14			Storefront/ Metal Panels-Salem																											
Phase 5 Priority A South Measure Panels	2	2	2023-02-02	2023-02-03			Storefront/ Metal Panels-Salem																											
Phase 5 Priority B South Flashing, Girt and insulation	15	3	2023-02-06	2023-02-24			Storefront/ Metal Panels-Salem																											
Phase 5 Priority B South Measure Panels	2	2	2023-02-14	2023-02-15			Storefront/ Metal Panels-Salem																											
? Pending Rigging route			2023-02-08	2023-02-08			GC - Gilbane																											
Bldg C ↕	37		2023-01-16	2023-02-21																														
C4 - tape walls and soffits	6	2	2023-01-16	2023-01-23	2023-01-16	2023-01-23	Carpentry-Central Ceilings																											
Close bldg C shaft/ walls	2	2	2023-01-23	2023-01-31	2023-01-21	2023-01-23	Carpentry-Central Ceilings																											
C1- hang drywall	6	2	2023-01-23	2023-01-30	2023-01-23	2023-01-30	Carpentry-Central Ceilings																											

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13																											
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18																						
Gym- in wall blocking	4	1	2023-01-25	2023-01-30	2023-01-25	2023-01-30	Carpentry-Central Ceilings																																																	
Gym- frame ceilings/ soffits	5	2	2023-01-27	2023-02-02	2023-01-27	2023-02-02	Carpentry-Central Ceilings																																																	
C1 - hang ceilings and soffits	3	2	2023-01-30	2023-02-01	2023-01-30	2023-02-01	Carpentry-Central Ceilings																																																	
Gym- Hang Drywall	5	4	2023-02-01	2023-02-07			Carpentry-Central Ceilings																																																	
C1 - tape walls and soffits	6	2	2023-02-02	2023-02-09			Carpentry-Central Ceilings																																																	
Remainder C2 drywall	5	3	2023-02-02	2023-02-08			Carpentry-Central Ceilings																																																	
Gym- frame ceilings/ soffits	5	2	2023-02-03	2023-02-09			Carpentry-Central Ceilings																																																	
Gym- Hang Drywall	5	4	2023-02-08	2023-02-14			Carpentry-Central Ceilings																																																	
C1 - sound/fire caulk	4	1	2023-02-10	2023-02-15			Carpentry-Central Ceilings																																																	
Gym- frame ceilings/ soffits	5	2	2023-02-10	2023-02-16			Carpentry-Central Ceilings																																																	
Remainder C3 drywall	5	3	2023-02-13	2023-02-17			Carpentry-Central Ceilings																																																	
Tape Gym Walls	5	1	2023-02-15	2023-02-21			Carpentry-Central Ceilings																																																	
C2- Ceiling Grid	5	1	2023-01-23	2023-01-27	2023-01-23	2023-01-27	Ceilings-Cheviot																																																	
C3- Ceiling Grid	5	1	2023-01-23	2023-01-27	2023-01-23	2023-01-27	Ceilings-Cheviot																																																	
C3- Ceiling Grid	5	1	2023-01-30	2023-02-03	2023-01-30	2023-02-03	Ceilings-Cheviot																																																	
C4- Ceiling Grid	5	1	2023-01-30	2023-02-03			Ceilings-Cheviot																																																	
C4- Ceiling Grid	5	1	2023-02-06	2023-02-10			Ceilings-Cheviot																																																	
Level-0 - Install OH Electric Rough In Pending predecessor activity completion - weather tight building	10	2	2023-01-19	2023-02-01	2023-01-19	2023-02-01	Electrical-Griffin																																																	
Level-0 - Install OH Electric Rough In Large Gym Pending predecessor activity completion - weather tight building	8	2	2023-01-30	2023-02-08			Electrical-Griffin																																																	
Level 1 music rooms A/V devices	2	2	2023-02-01	2023-02-02			Electrical-Griffin																																																	
Gym A/V conduits	7	2	2023-02-06	2023-02-14			Electrical-Griffin																																																	
Gym- Ceiling Boxes	4	2	2023-02-14	2023-02-17			Electrical-Griffin																																																	
HOLD- Gym Equipment Supports	5	0	2023-02-06	2023-02-10			GC - Gilbane																																																	
Ceiling Inspection C2			2023-02-17	2023-02-17			GC - Gilbane																																																	

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23					Week Of Mon Jan 30					Week Of Mon Feb 06					Week Of Mon Feb 13				
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11
Gym- Sprinkler Drops	3	2	2023-02-15	2023-02-17			JCI- Fire Protection																				
Corner C- Masonry (Hydro)	5	2	2023-01-19	2023-01-24	2023-01-19	2023-01-25	Masonry-Fernandes																				
Corner C- Masonry	5	5	2023-01-19	2023-01-25	2023-01-19	2023-01-25	Masonry-Fernandes																				
Wash- Corner C	3	1	2023-01-28	2023-01-28	2023-01-28	2023-01-31	Masonry-Fernandes																				
Install Playground Equip. Supports	5	3	2023-02-06	2023-02-10			Misc Metal-United																				
C3- Paint	5	2	2023-01-18	2023-01-24	2023-01-18	2023-01-24	Paint- Color Concepts																				
C4- Paint	5	2	2023-01-24	2023-01-30			Paint- Color Concepts																				
Pre-K Roof Install	5	7	2023-02-13	2023-02-17			Roofing- JD Rivet																				
Balance of Release #1 Frames	5	2	2023-02-03	2023-02-09			Storefront/ Metal Panels-Salem																				
Balance of Release #1 Glazing	5	2	2023-02-10	2023-02-16			Storefront/ Metal Panels-Salem																				

Crew Size By Role						Project Role	Week Of Mon Jan 23					Week Of Mon Jan 30					Week Of Mon Feb 06					Week Of Mon Feb 13										
		Total	Complete	Promised Incomplete	Remaining		23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17

All Roles ⌵	2,480	523 (21%)	1,598 (64%)	359 (14%)		106	100	110	98	102	6	126	104	111	111	115	145	155	158	155	157	141	138	124	117	101
	178	29 (16%)	105 (59%)	44 (25%)	APEX - HVAC	7	7	7	4	4		5	5	5	5	5	11	11	13	13	16	15	15	11	11	8
	966	227 (23%)	579 (60%)	160 (17%)	Carpentry-Central Ceilings	38	30	37	33	37		50	40	48	51	47	61	63	61	64	65	52	52	47	46	44
	35	15 (43%)	10 (29%)	10 (29%)	Ceilings-Cheviot	2	2	2	2	2		2	2	2	2	2	1	1	1	1	1	2	2	2	2	2
	22	0 (0%)	22 (100%)	0 (0%)	Concrete-Marguerite												3	7	4	4	4					
	325	53 (16%)	216 (66%)	56 (17%)	Electrical-Griffin	11	11	11	13	13		14	14	18	14	12	16	18	22	14	14	22	24	20	22	22
	4	0 (0%)	4 (100%)	0 (0%)	Fireproofing-Ricmor				2	2																
	23	3 (13%)	20 (87%)	0 (0%)	GC - Gilbane	1	1	1				2	2	2	2	2	2	2	2	2	2					
	16	0 (0%)	4 (25%)	12 (75%)	JCI- Fire Protection											2	2				2	2	4	2	2	
	219	54 (25%)	155 (71%)	10 (5%)	Masonry-Fernandes	17	17	17	10	10	1	11	11	10	10	10	10	10	14	17	17	7	5	5	5	5
	97	30 (31%)	67 (69%)	0 (0%)	Mechanical-PJ Kennedy	5	5	5	5	5		7	7	7	7	7	8	8	6	5	5	5				
	47	0 (0%)	47 (100%)	0 (0%)	Misc Metal-United			4	4	4		4	4	4	4	4	3	3	3	3	3					
	45	4 (9%)	21 (47%)	20 (44%)	Paint- Color Concepts	2	4	2	2	2		2			1		2	2	2	2	2	4	4	4	4	4
	89	26 (29%)	55 (62%)	8 (9%)	Plumbing-PJ Kennedy	5	5	2	4	4		2	2	2	4	4	7	7	7	7	7	4	4	4	4	4
	155	50 (32%)	70 (45%)	35 (23%)	Roofing- JD Rivet	6	6	6	6	6	5	9	3	3		7	7	7	7	7	7	14	14	14	14	7

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role	Week Of Mon Jan 23							Week Of Mon Jan 30							Week Of Mon Feb 06							Week Of Mon Feb 13									
								23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18				
		259		32 (12%)	223 (86%)	4 (2%)	Storefront/ Metal Panels- Salem	12	12	16	13	13				18	14	10	11	13				12	16	16	16	14				14	16	13	7	3		

Generated on: February 02, 2023 08:54:36 AM EST

Italic indicates a constraint.

