

## PIERCE SCHOOL WEEKLY UPDATE, 05/09/25



**PLEASE NOTE: SCHOOL ST WILL BE REDUCED TO ONE-LANE TRAFFIC ON 5/20 FROM 8:30AM-3:30PM DAILY**

### **THIS WEEK (May 12-16)**

- Excavate and truck out soil.
- Build footings along A line
- Prep for footings along 1/1.3 lines
- Remove/remediate windows at Historic Bldg

### **PROJECT TRACKING:**

- Concrete footings: 5%

### **ANTICIPATING NEXT WEEK (May 19-23)**

- Begin cut and cap work in School Street
- Layout and prep for footings
- FRP (form, rebar, pour) footings

### **MILESTONES:**

- Start concrete footings: 5/19/25 5/16/25

### **Narrative:**

This week we finished the mass excavation of the site – export will continue as soil is removed for footings. Forms and rebar began for the footings along A line, with our first concrete pour scheduled for Monday, 5/19. There have been multiple testing agencies on site all week, reviewing soil conditions and testing compaction levels for the area underneath future footings.




Eight (8) windows were removed from the Historic Building (all will eventually be replaced) for the Design Team to confirm details. Next week we will see trucks for soil export and structural fill import. Prep, layout, forms and rebar for footings will continue, and we expect concrete pours on Monday and Friday of next week, weather permitting.


Overall, the project remains on schedule. See page 2 for a graphic showing footing progress.

For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



-  Footing/Site Prep
-  Footings
-  Foundation Walls

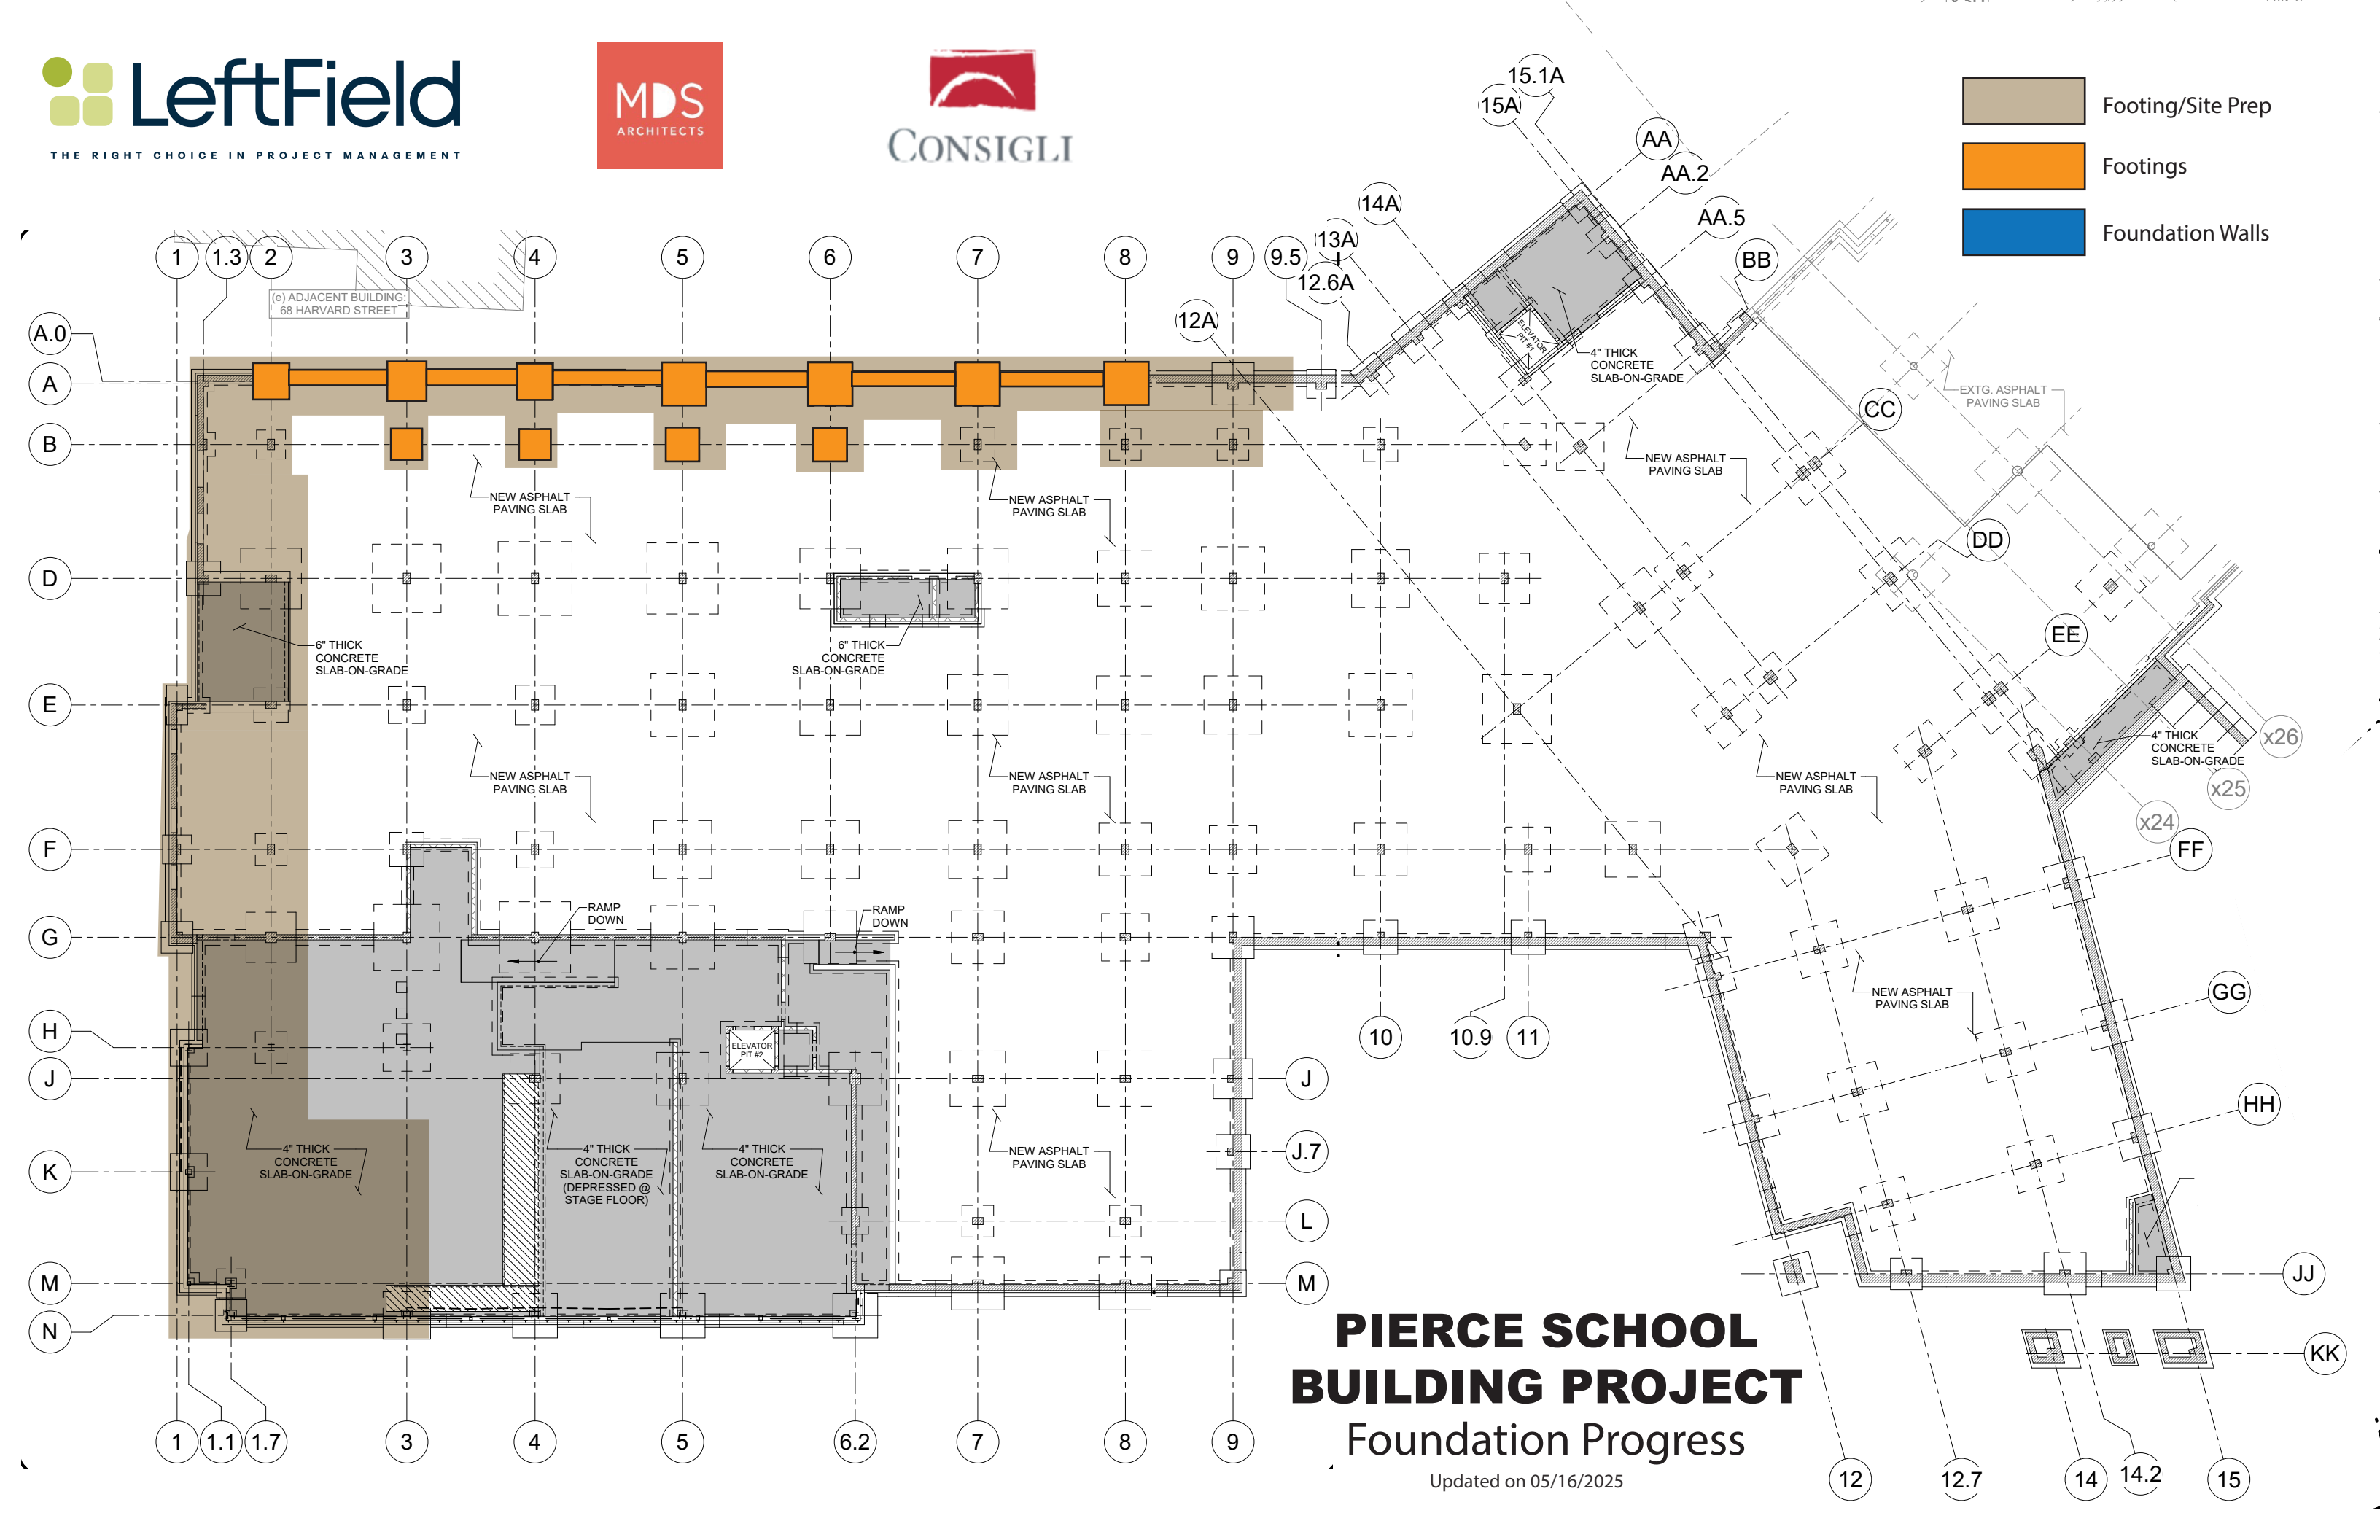

**PIERCE SCHOOL  
BUILDING PROJECT**  
Foundation Progress

Updated on 05/16/2025
