

## PIERCE SCHOOL WEEKLY UPDATE, 06/06/25



**PLEASE NOTE: UTILITY WORK WILL BE ON HARVARD ST FROM 8:30AM-3:30PM DAILY**

### **THIS WEEK** (June 2-6)

- Excavate and truck out soil
- Form/Rebar/Pour walls along A line
- F/R/P footings along 1/1.3/2 lines
- Prep for footings along G-N, 1-6 lines
- Cut and cap utilities in School Street

### **PROJECT TRACKING:**

- Concrete footings: 12%

### **ANTICIPATING NEXT WEEK** (June 9-13)

- Cut and cap work moves to Harvard Street
- Footing prep/layout G-N, 1-6 lines
- F/R/P footings and walls 'A', 1/1.3, 'N' lines
- Treat and pump out site pond (per DEP regs)

### **MILESTONES:**

- Complete concrete walls 'A' side: 07/11/25

### Narrative:

Concrete pours for footings and walls continued this week along the perimeter of the building (see next page for graphic). The site contractor continued with excavation, fill and compaction for the next areas of foundation work, generally along School Street where the Multipurpose Room will be located.

Inspections continued daily for compaction, rebar, concrete and bottom of footings.

Equipment was set up to begin treatment and removal of the site pond (rainwater) next week. Water testing, inspections, and coordination with the Town will occur before any removal begins.

A Utility crew completed (for now) cut and cap work on School Street and will begin onto Harvard Street next week.


NOTE: BEGINNING ON JUNE 25<sup>TH</sup>, SCHOOL STREET BETWEEN WASHINGTON AND HARVARD STREETS WILL BE CLOSED FROM 7AM-4PM DAILY, THROUGH THE SUMMER.




Overall, the project remains on schedule.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>

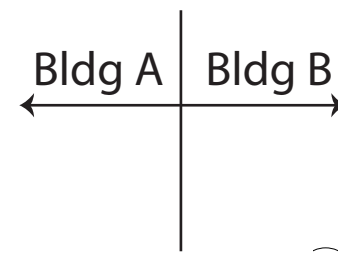



-  Footing/Site Prep
-  Footings
-  Foundation Walls

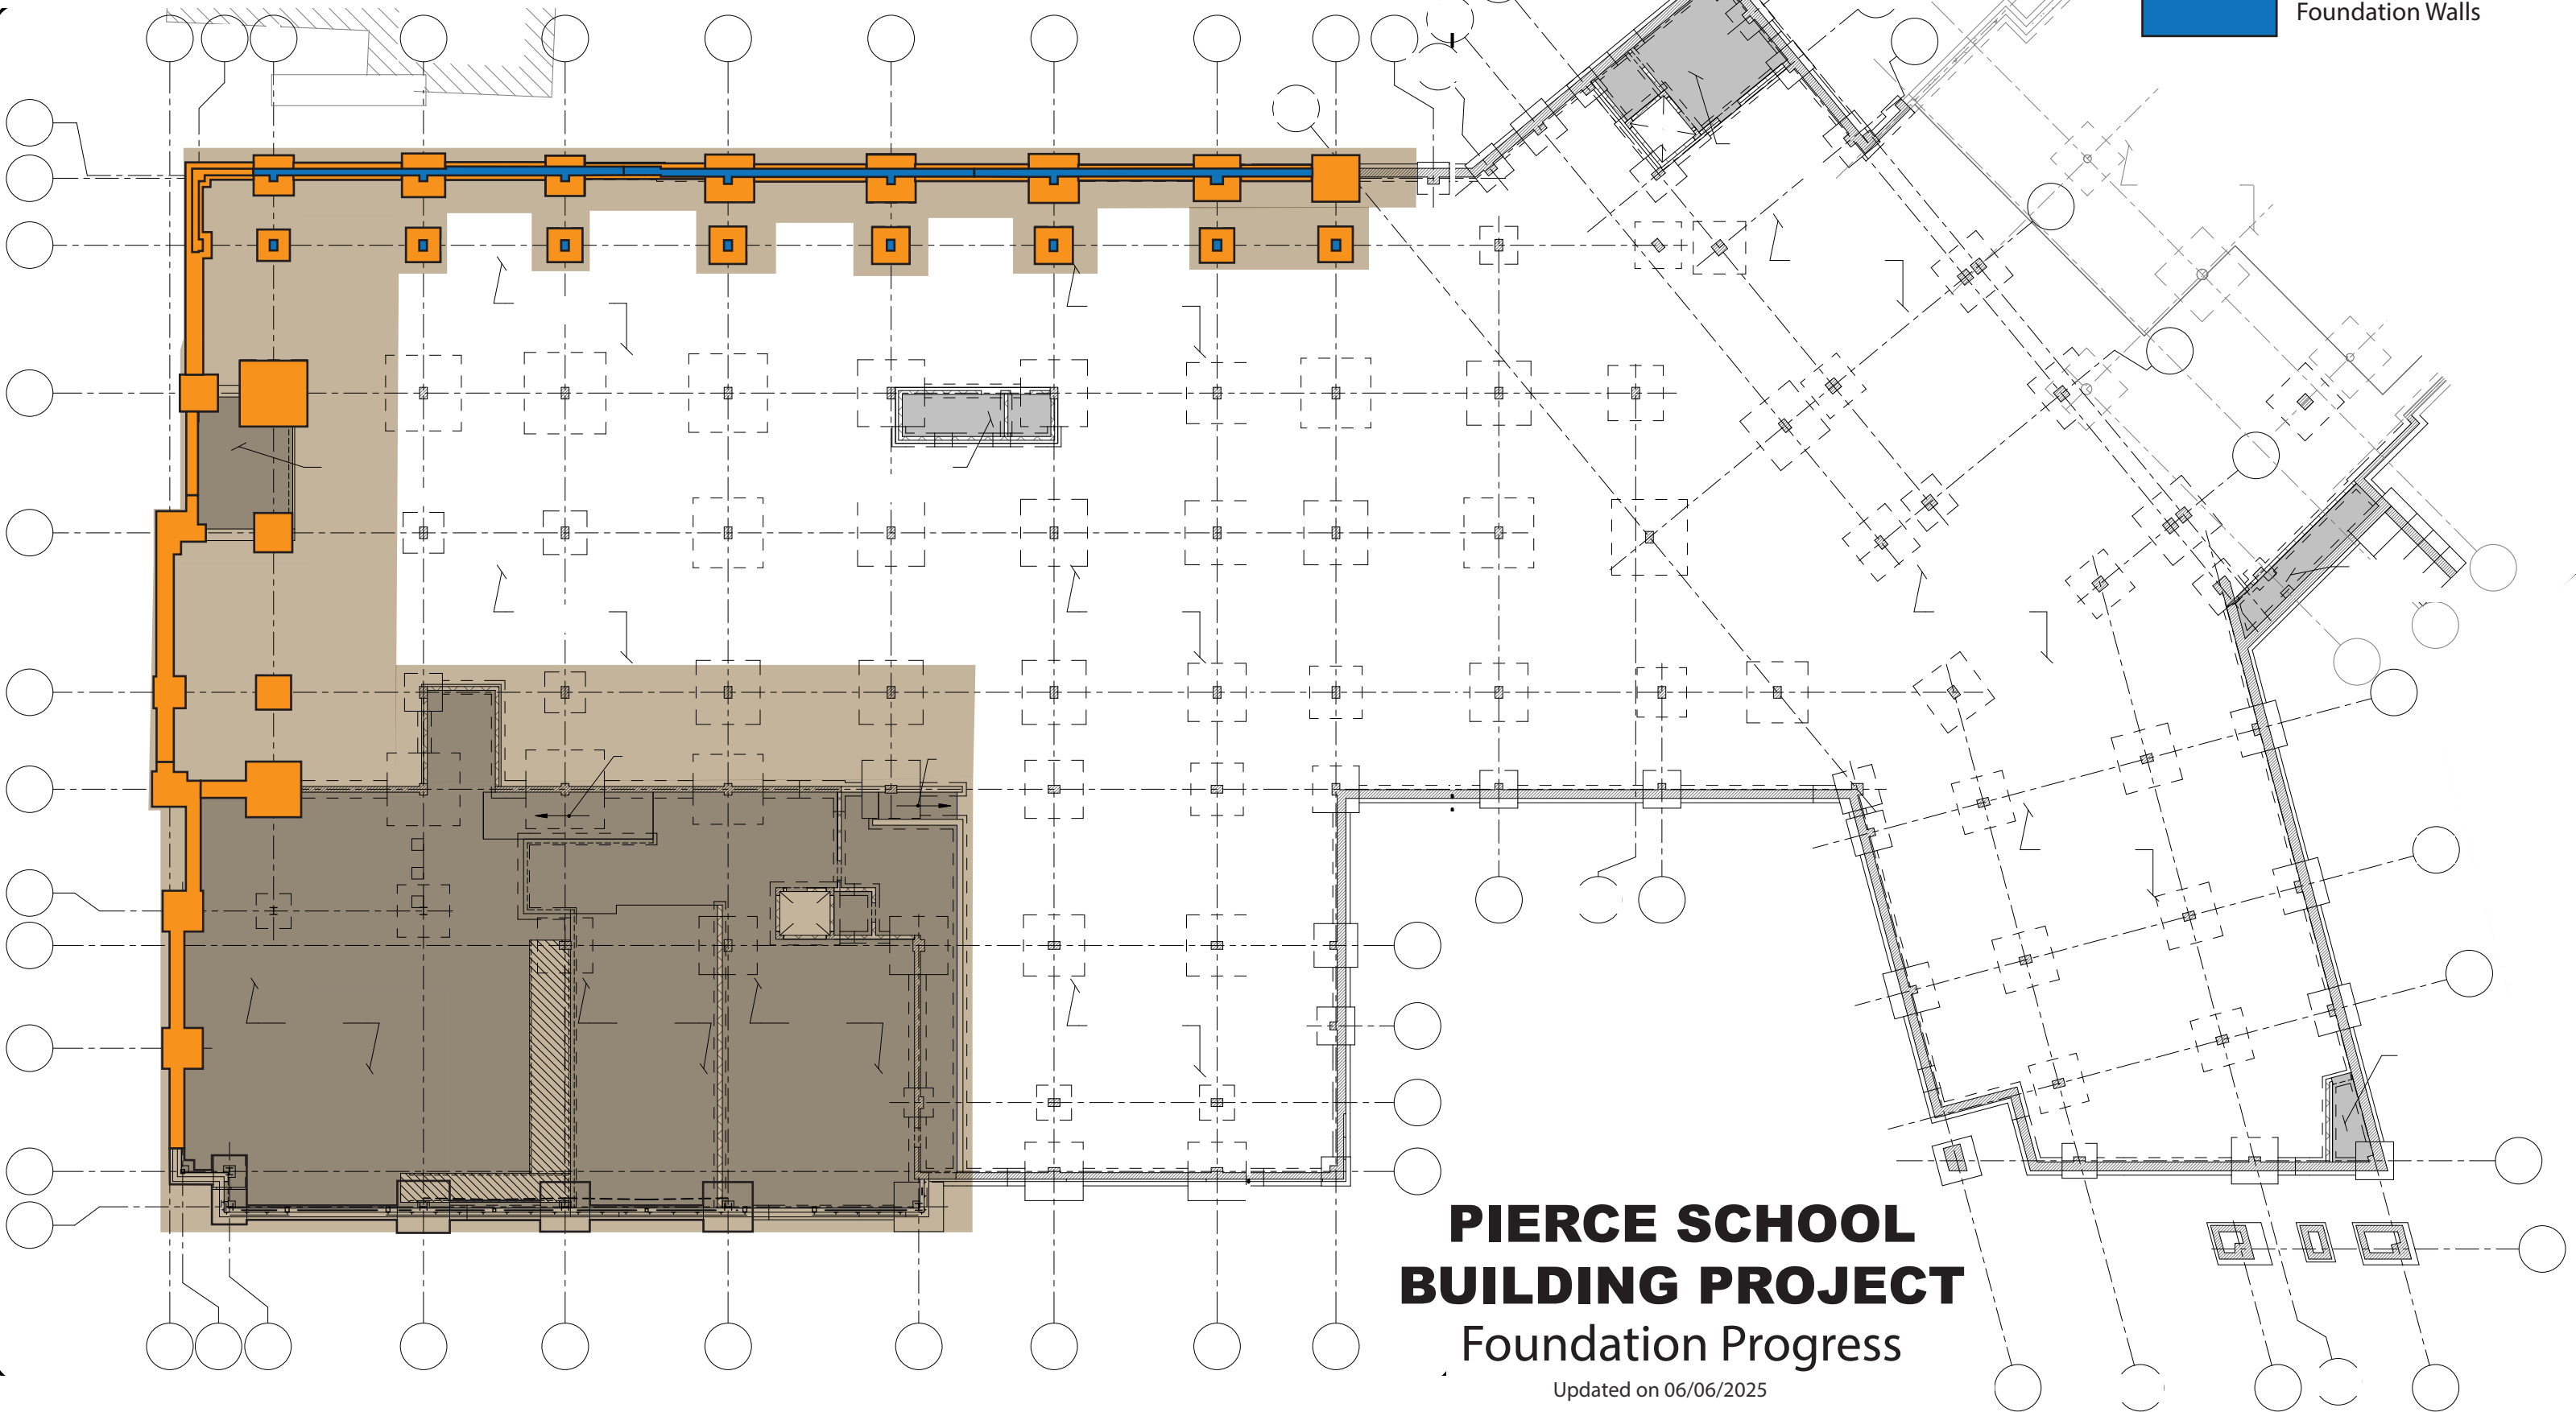

**PIERCE SCHOOL  
BUILDING PROJECT**  
Foundation Progress

Updated on 06/06/2025
