

PIERCE SCHOOL WEEKLY UPDATE, 10/03/25



THIS WEEK (Sept. 29-Oct. 3)

- Form/Rebar/Pour high walls
- Steel erection ongoing, Bldg A
- Coring and conduit work in elect. room/Xfrmer
- Exterior material installation at mock-up
- Selective demolition at Historic Building
- Sewer work in Pierce Street

PROJECT TRACKING:

- Footings: 95%; walls: 85%; columns: 95%

ANTICIPATING NEXT WEEK (October 6-10)

- Steel erection and metal deck ongoing
- F/R/P walls in Building B
- Exterior material install at mock-up
- Selective demo, foundation work in Hist. Bldg
- Continue sewer work in Pierce Street

MILESTONES:

- Deck pours #5, 6, 7: 10/27, 10/29, 10/30
- Steel erection Bldg A Phase 1: 11/04/25

Narrative:





Two sections of concrete walls were poured this week, as well as some of the remaining footings in Building B. Steel erection made excellent progress in Building A (see photo); they will continue next week with both steel and metal deck. Footings in Building B were formed and poured; progress continued on the footings for the large retaining wall, and the utility crew on Pierce Street excavated nearly half of the route. The electricians have the conduit and related work for the transformer completed, and the pad is on site. Brick work was completed at the mock-up, and the next round of materials including stone and metal panels are being installed this week; that work will continue through next week. Work continued inside the Historic Building with selective demolition and the installation of shoring. Overall, the project remains on schedule.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



Bldg A Bldg B

-  Footing/Site Prep
-  Footings
-  Foundation Walls
-  Structural Slab

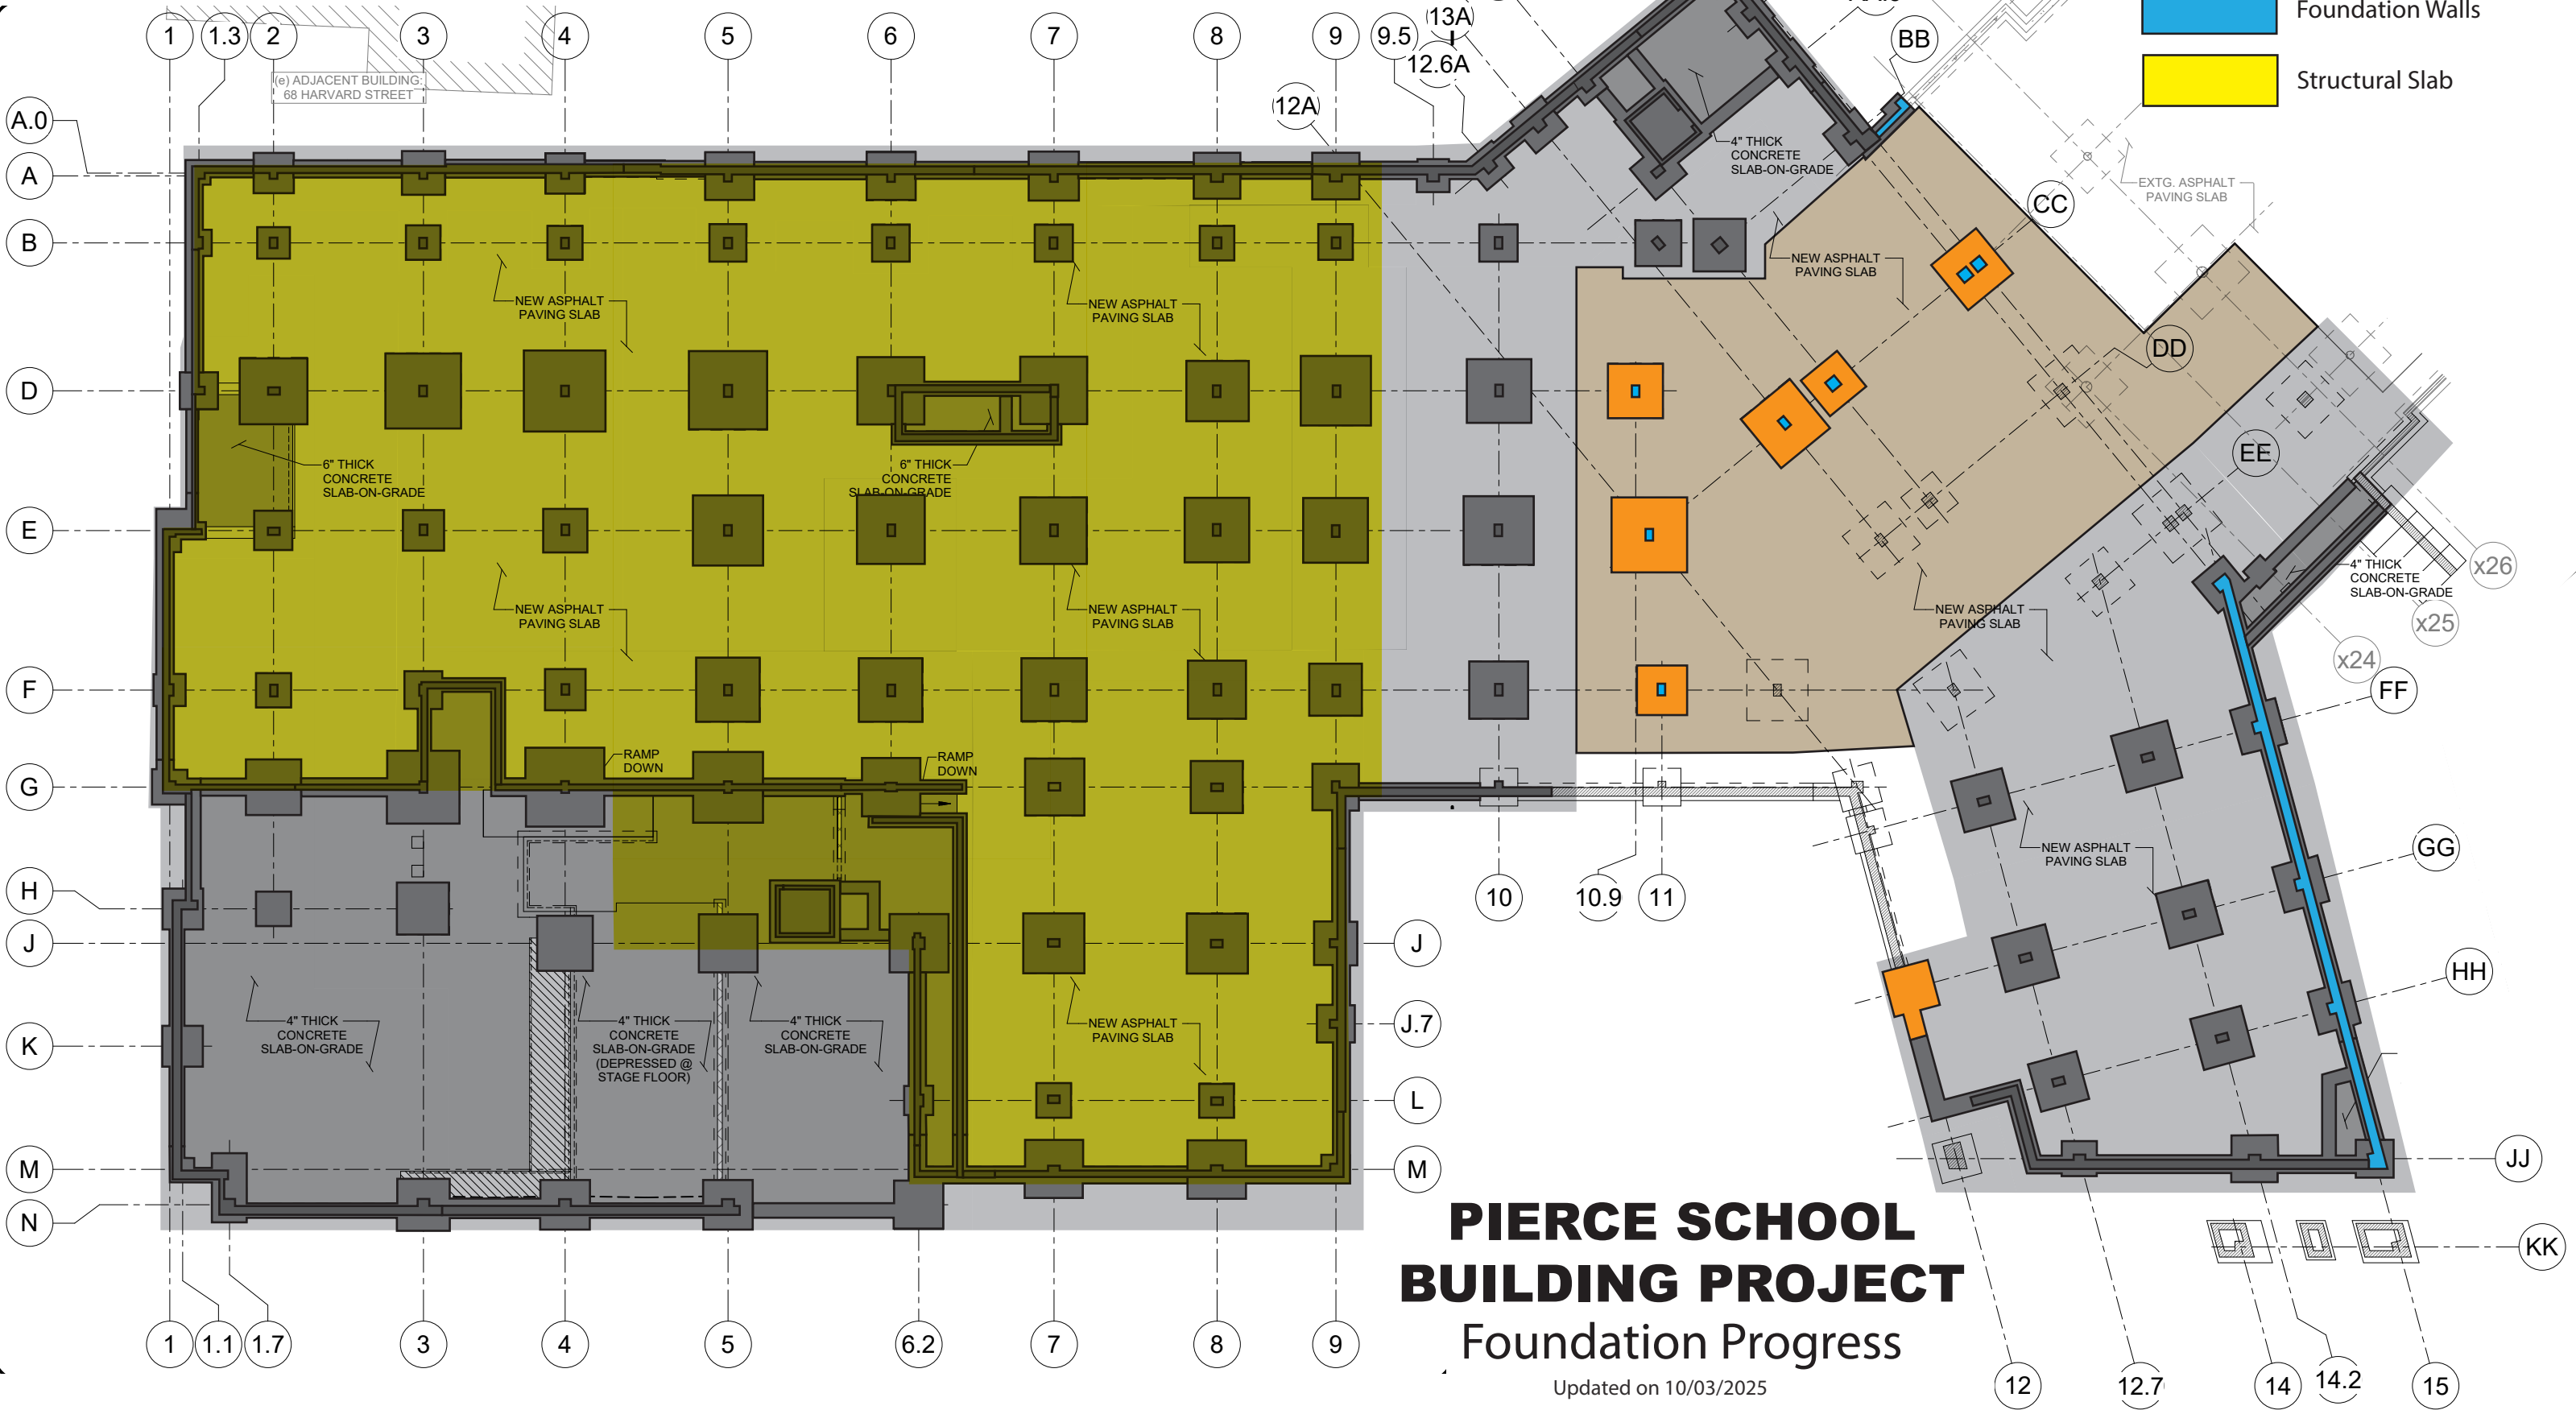

**PIERCE SCHOOL
BUILDING PROJECT**
Foundation Progress

Updated on 10/03/2025
