


## PIERCE SCHOOL WEEKLY UPDATE, 10/17/25

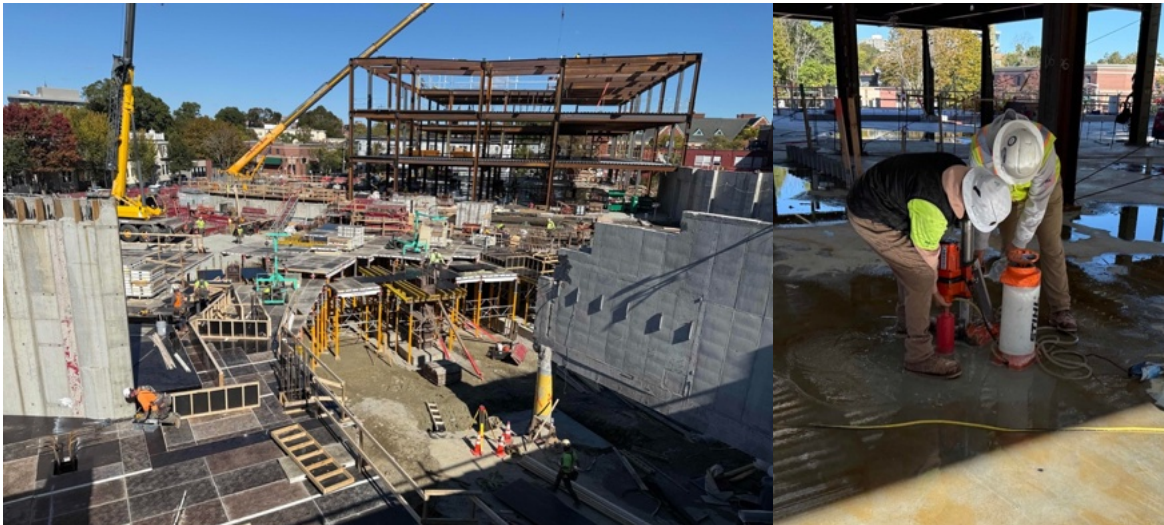

### THIS WEEK (October 13-17)

- Complete footings and columns in Bldg B
- Steel erection, metal deck ongoing, Bldg A
- Peri deck connected between Bldgs A and B
- Temp lighting, power to new building
- Pit excavation at Historic Building finished
- Sewer work in Pierce Street ongoing

### PROJECT TRACKING:

- Footings: 100%; walls: 90%; columns: 100%

### ANTICIPATING NEXT WEEK (October 13-17)

- Steel erection and metal deck ongoing
- Install rebar for Pour #5
- Sealants at mock-up
- Begin foundation work at Hist. Bldg.
- Continue sewer work in Pierce Street

### MILESTONES:

- Deck pours #5, 6, 7: 11/3, 11/5, 11/7
- Steel erection Bldg A Phase 1: 11/04/25

### Narrative:

The last footings and columns were poured this week, and the footing for the retaining wall was also placed.

Peri deck for the elevated structural deck was connected from Building A to Building B. Rebar for the next deck pours was begun.

Steel erection made excellent progress again in Building A, including the roof steel at the mechanical area. The crane was relocated to install the next round of structural steel along the Multipurpose Room.

The utility crew on Pierce Street continued their work on the sewer line without any issues. The site contractor has moved to the Pierce Street side of the building to start perimeter drainage and backfilling.

The electricians have been working on temp lighting and wiring in Building A.

Exterior materials at the mock-up were completed this week.

Pits and underpinning in the Historic Building basement were completed this week.

Overall, the project remains on schedule.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



Bldg A    Bldg B  
←                      →

-  Footing/Site Prep
-  Footings
-  Foundation Walls
-  Structural Slab

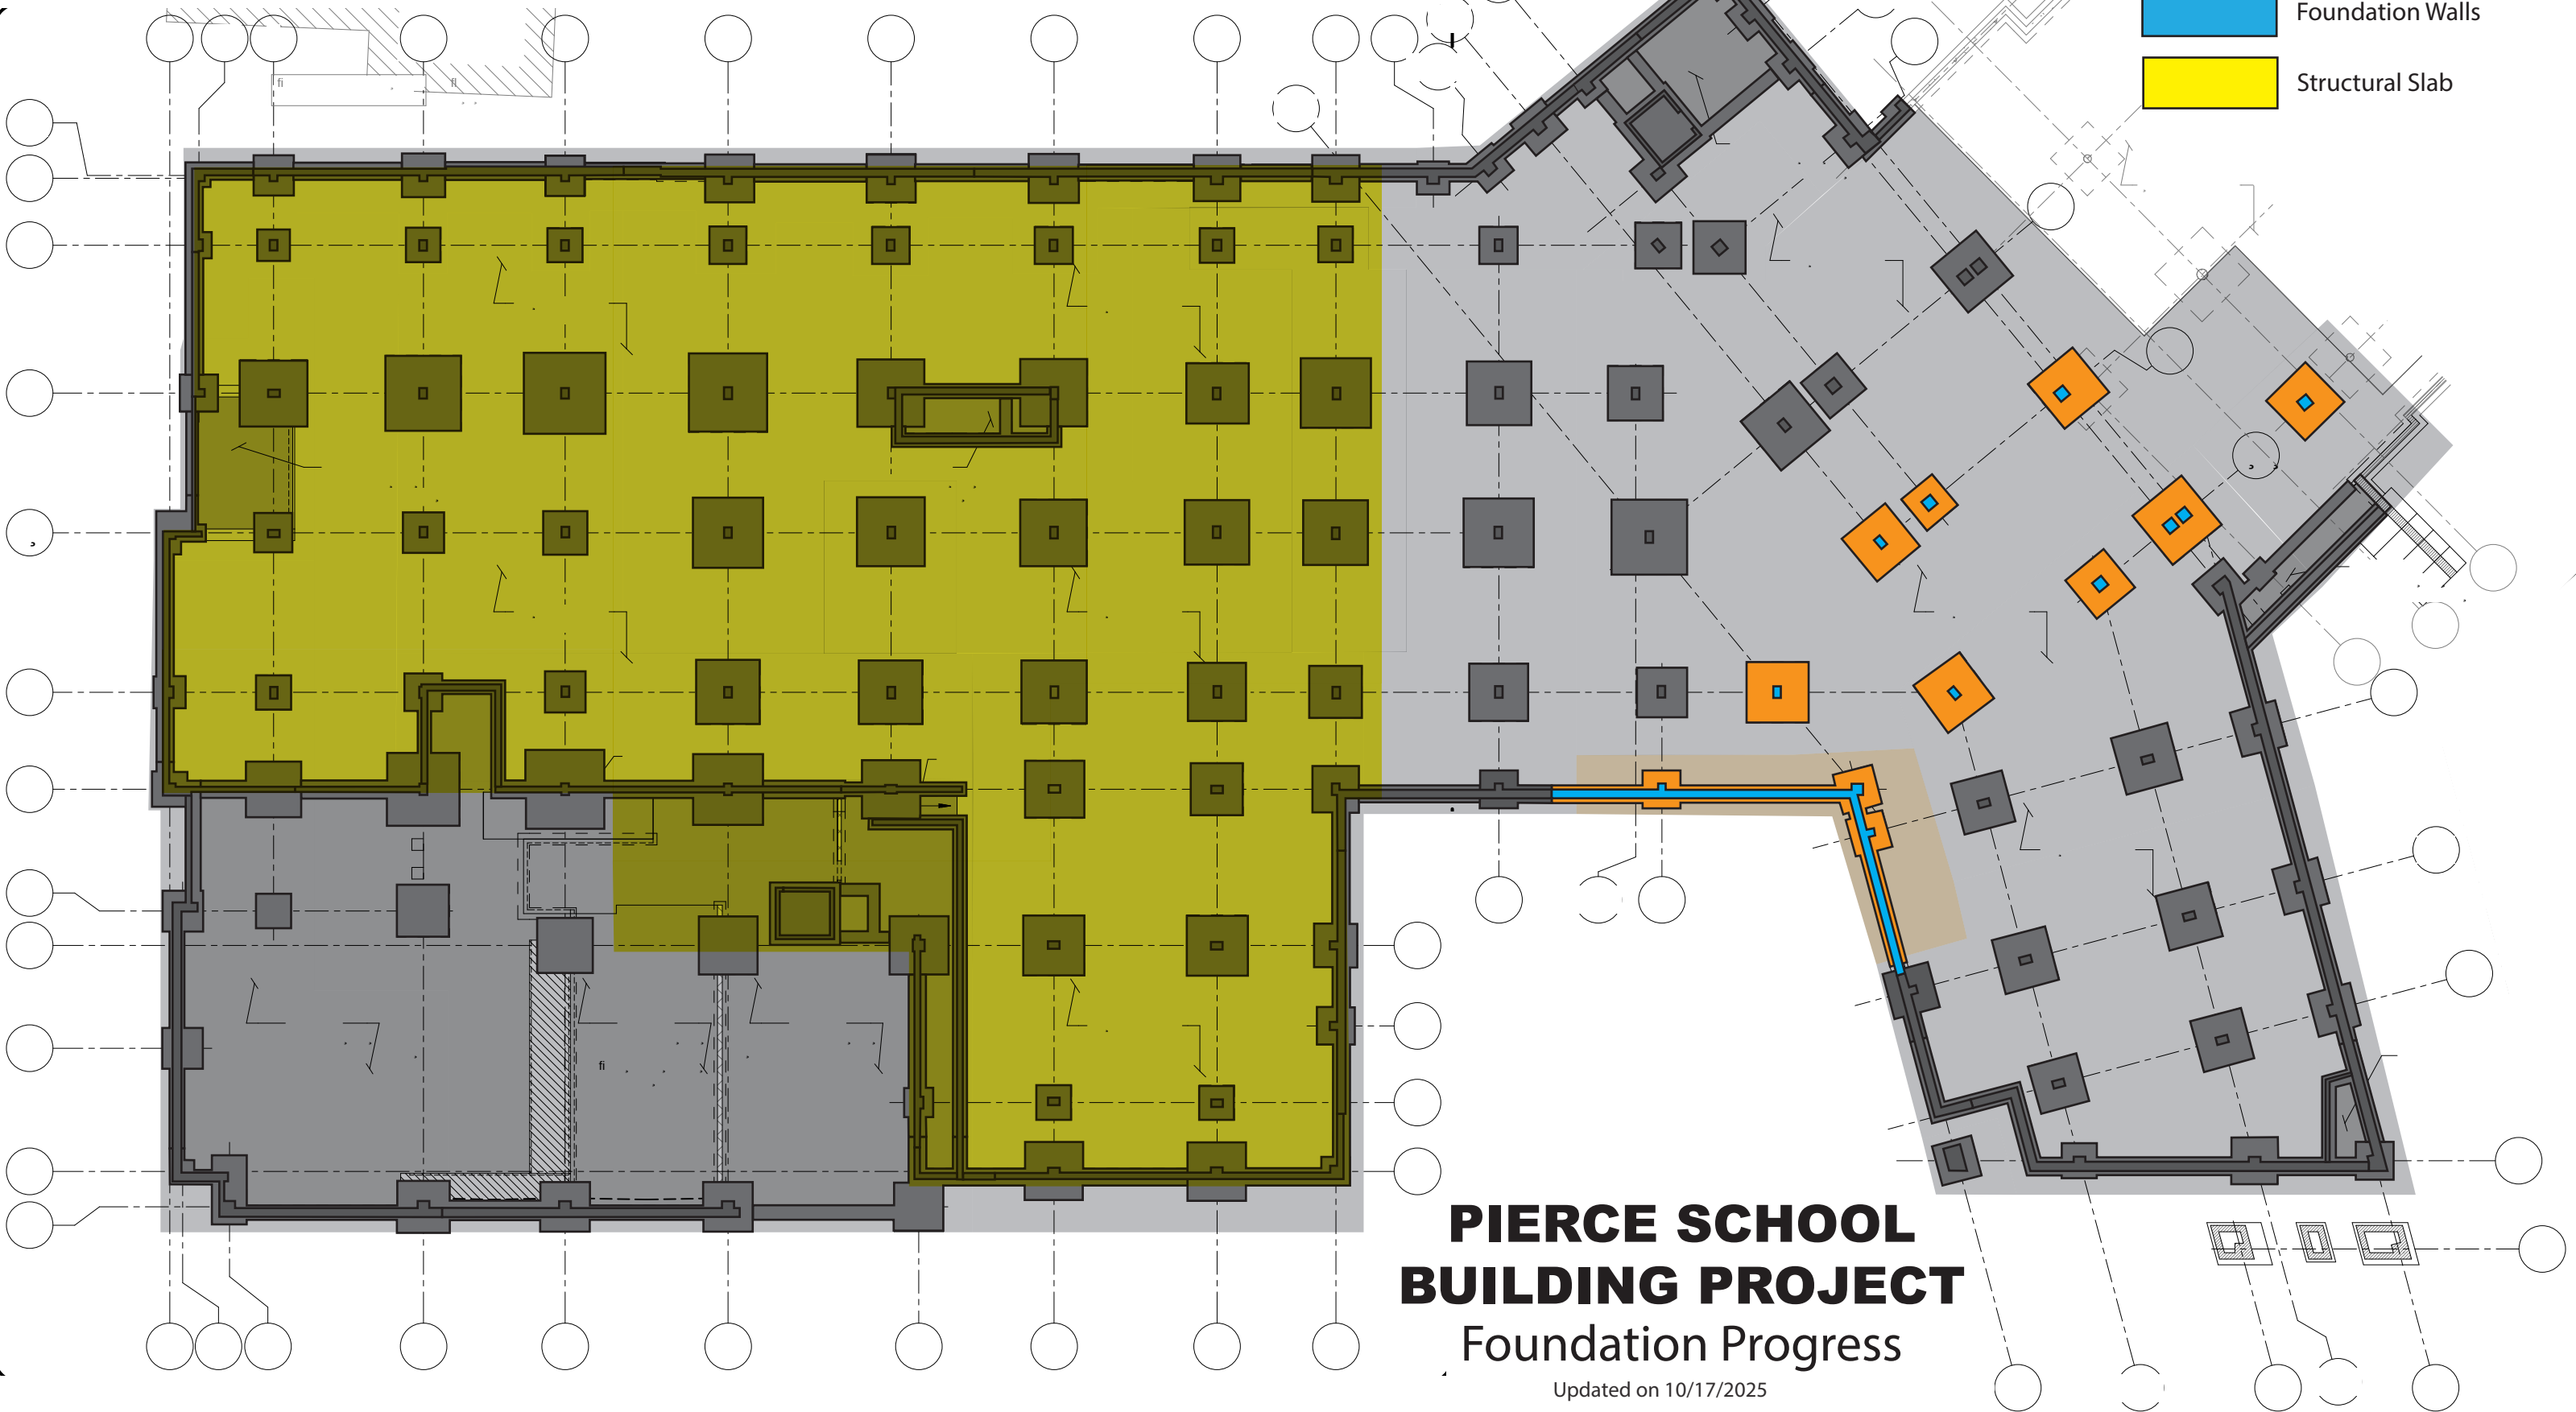

**PIERCE SCHOOL  
BUILDING PROJECT**  
Foundation Progress

Updated on 10/17/2025
