

PIERCE SCHOOL WEEKLY UPDATE, 05/23/25



PLEASE NOTE: SCHOOL ST WILL BE REDUCED TO ONE-LANE TRAFFIC FROM 8:30AM-3:30PM DAILY

THIS WEEK (May 19-23)

- Excavate and truck out soil
- Pour concrete at footings along A line.
- Footing and wall forms/rebar along A line
- Prep for footings along 1/1.3 lines, N line

PROJECT TRACKING:

- Concrete footings: 5%

ANTICIPATING NEXT WEEK (May 27-31)

- Continue cut and cap work in School Street
- Footing prep/layout along N line
- FRP (form, rebar, pour) footings and walls

MILESTONES:

- Complete concrete walls 'A' side: 07/11/25

Narrative:

This week we had our first concrete pour for footings, along 'A' line. Forms and rebar continued for the footings along 'A' line and adjacent footings, turning the corner to 1/1.3 line. Wall panels and rebar cages were stood up on the newly poured footings. The existing rubble wall directly against a live utility duct bank was successfully removed, and excavation, fill and compaction for footings was begun along 1/1.3 line (parallel to Harvard St) to the corner of the building at School St ('N' line).

Inspections continued daily for compaction, rebar, concrete and bottom of footings.

Weather impacted our second concrete pour planned for Friday, but the crews continued with rebar and formwork.


A Utility crew began some preliminary work on School Street and will continue next week with cut and cap of utilities in the road.




Overall, the project remains on schedule. See page 2 for a graphic showing footing progress.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>

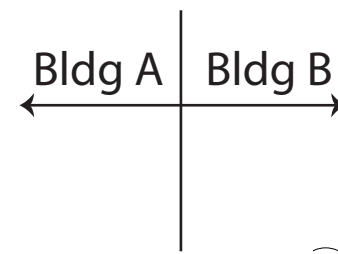



-  Footing/Site Prep
-  Footings
-  Foundation Walls

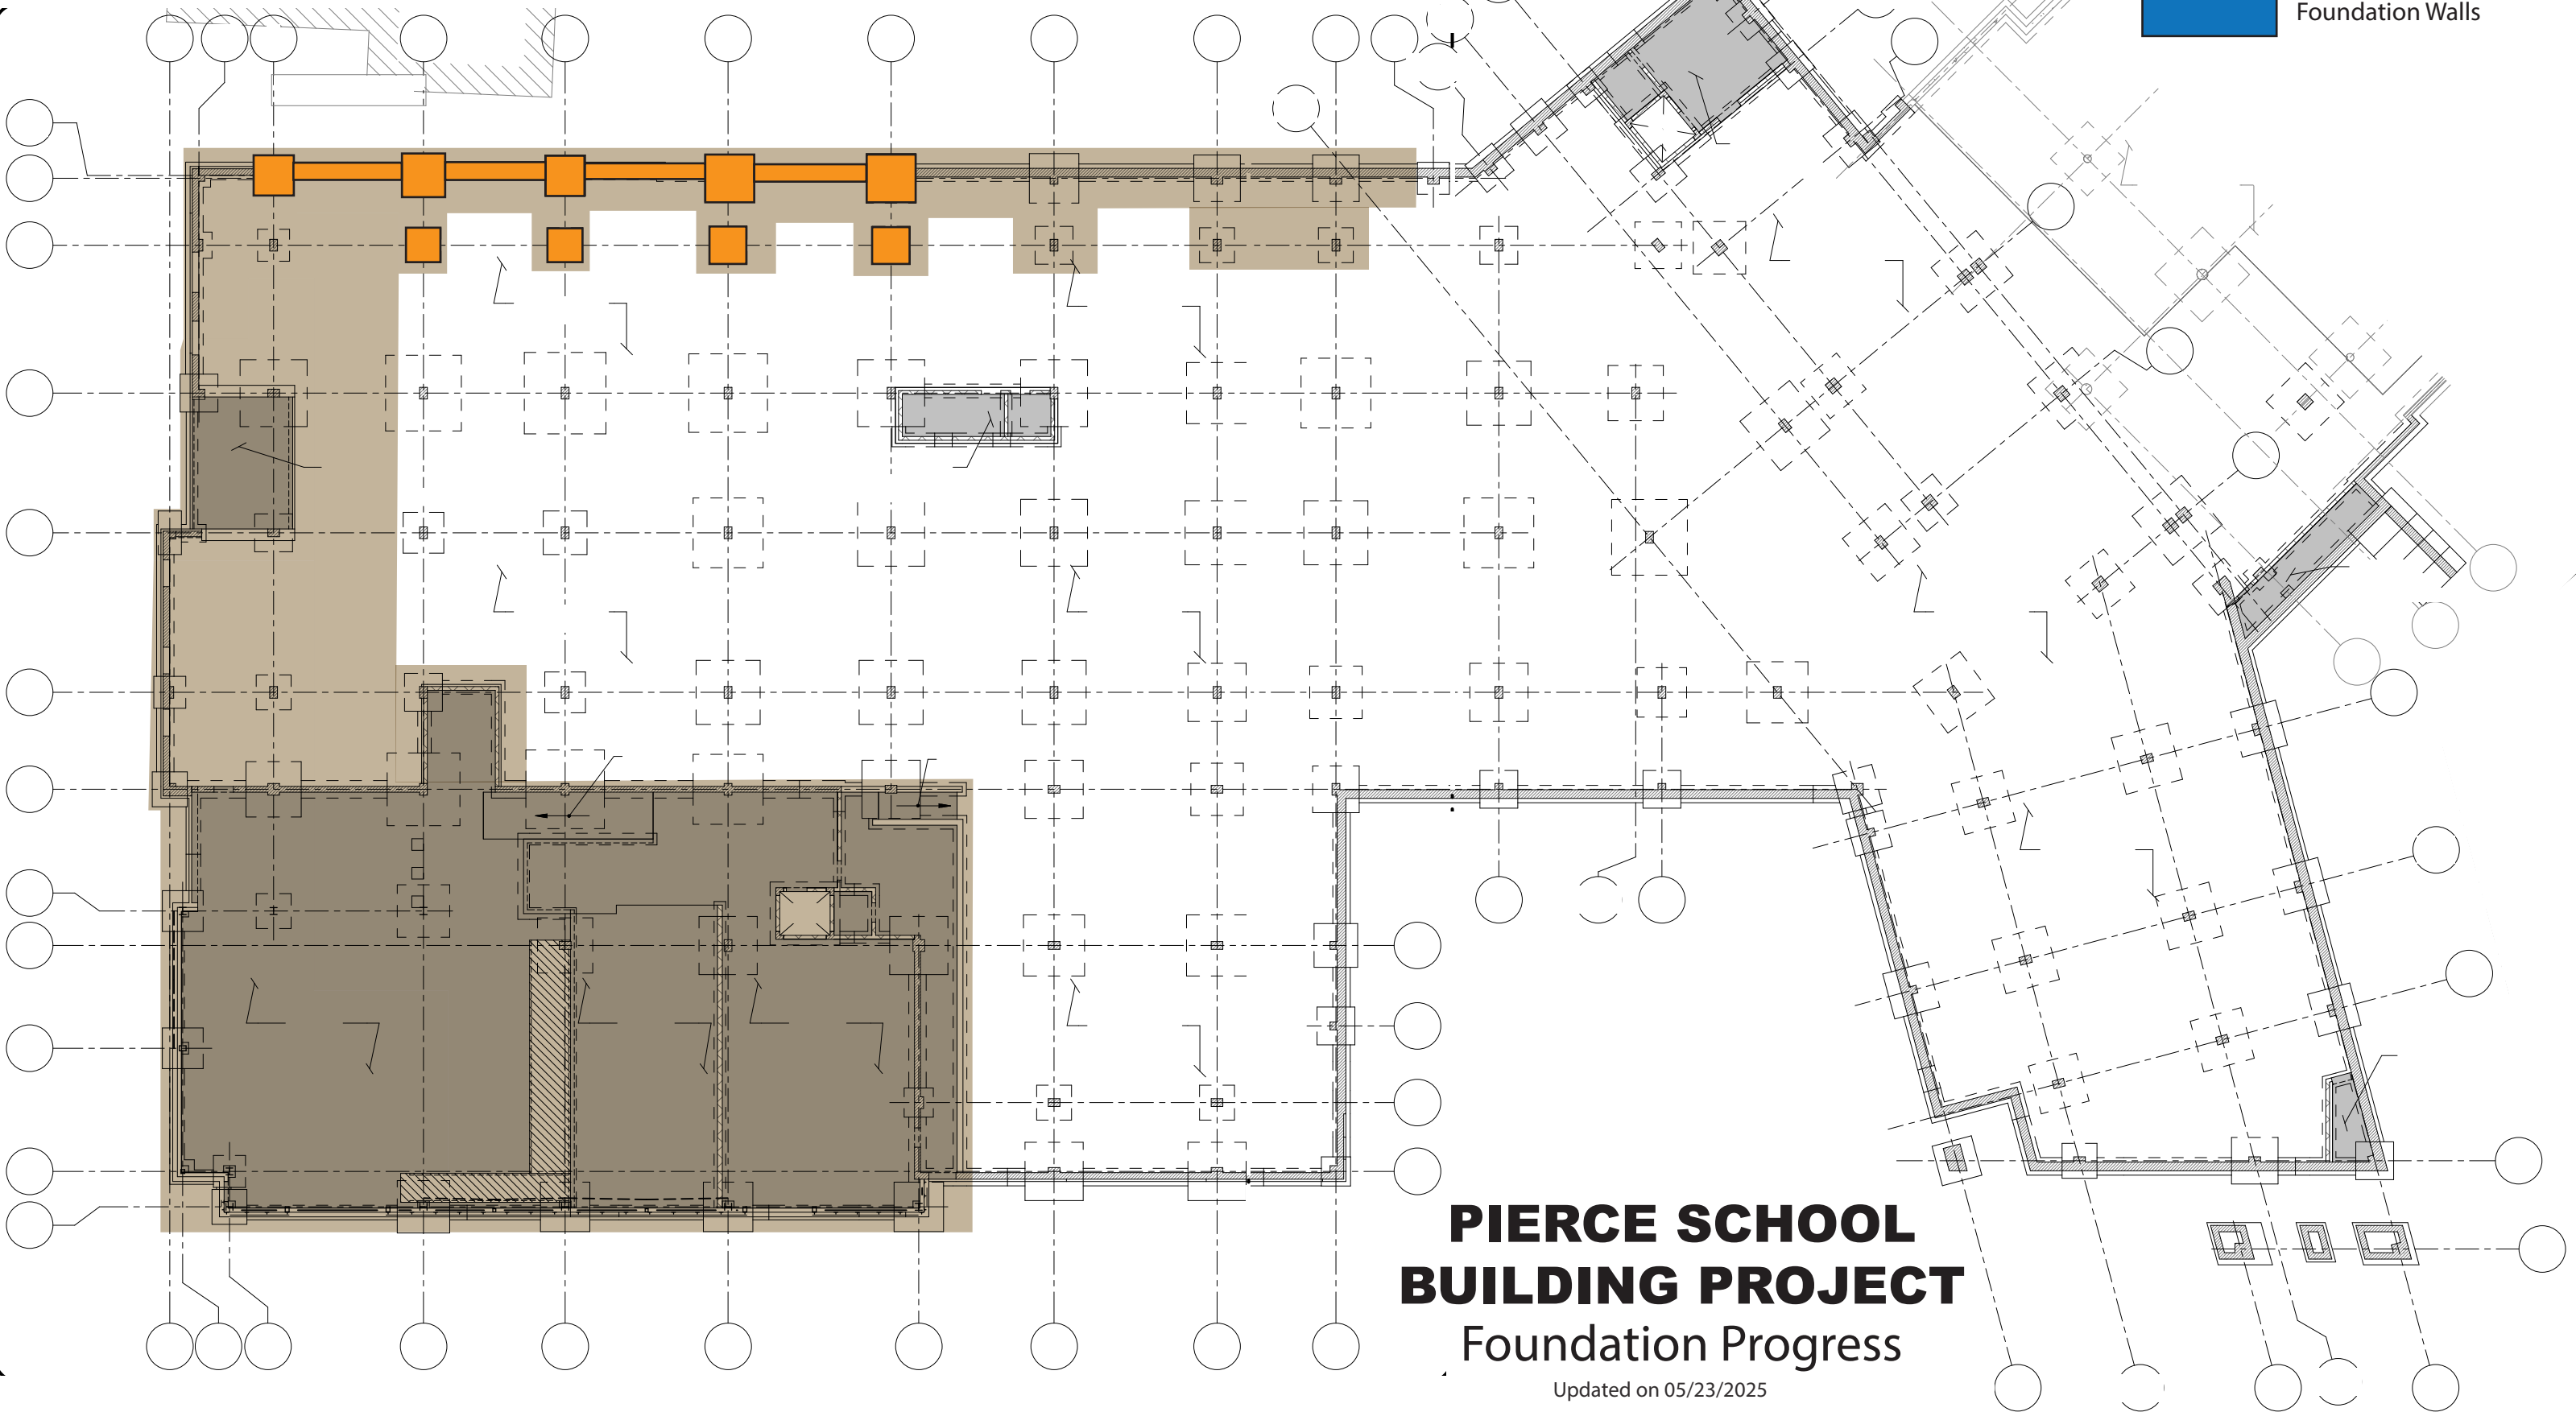

**PIERCE SCHOOL
BUILDING PROJECT**
Foundation Progress

Updated on 05/23/2025
