

PIERCE SCHOOL WEEKLY UPDATE, 05/30/25



PLEASE NOTE: SCHOOL ST WILL BE REDUCED TO ONE-LANE TRAFFIC FROM 8:30AM-3:30PM DAILY

THIS WEEK (May 27-30)

- Excavate and truck out soil
- Form/Rebar/Pour footings, walls along A line
- F/R/P footings along 1/1.3/2 lines
- Prep for footings along G-N, 1-6 lines
- Cut and cap utilities in School Street

PROJECT TRACKING:

- Concrete footings: 12%

ANTICIPATING NEXT WEEK (June 2-6)

- Continue cut and cap work in School Street
- Footing prep/layout G-N, 1-6 lines
- F/R/P footings and walls 'A' and 1/1.3 lines
- Install underground oil/gas separator

MILESTONES:

- Complete concrete walls 'A' side: 07/11/25

Narrative:

Concrete pours for footings and walls continued this week along the perimeter of the building (see next page for graphic). The site contractor continued with excavation, fill and compaction for the next areas of foundation work, generally along School Street where the Multipurpose Room will be located.

Inspections continued daily for compaction, rebar, concrete and bottom of footings.

A Utility crew continued with vacuum excavation on School Street to cut and cap utilities to Town standards; this work will continue for the next couple of weeks and will extend onto Harvard Street.


NOTE: BEGINNING ON JUNE 25TH, SCHOOL STREET BETWEEN WASHINGTON AND HARVARD STREETS WILL BE CLOSED FROM 7AM-4PM DAILY, THROUGH THE SUMMER.

Overall, the project remains on schedule.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>





- Footing/Site Prep
- Footings
- Foundation Walls

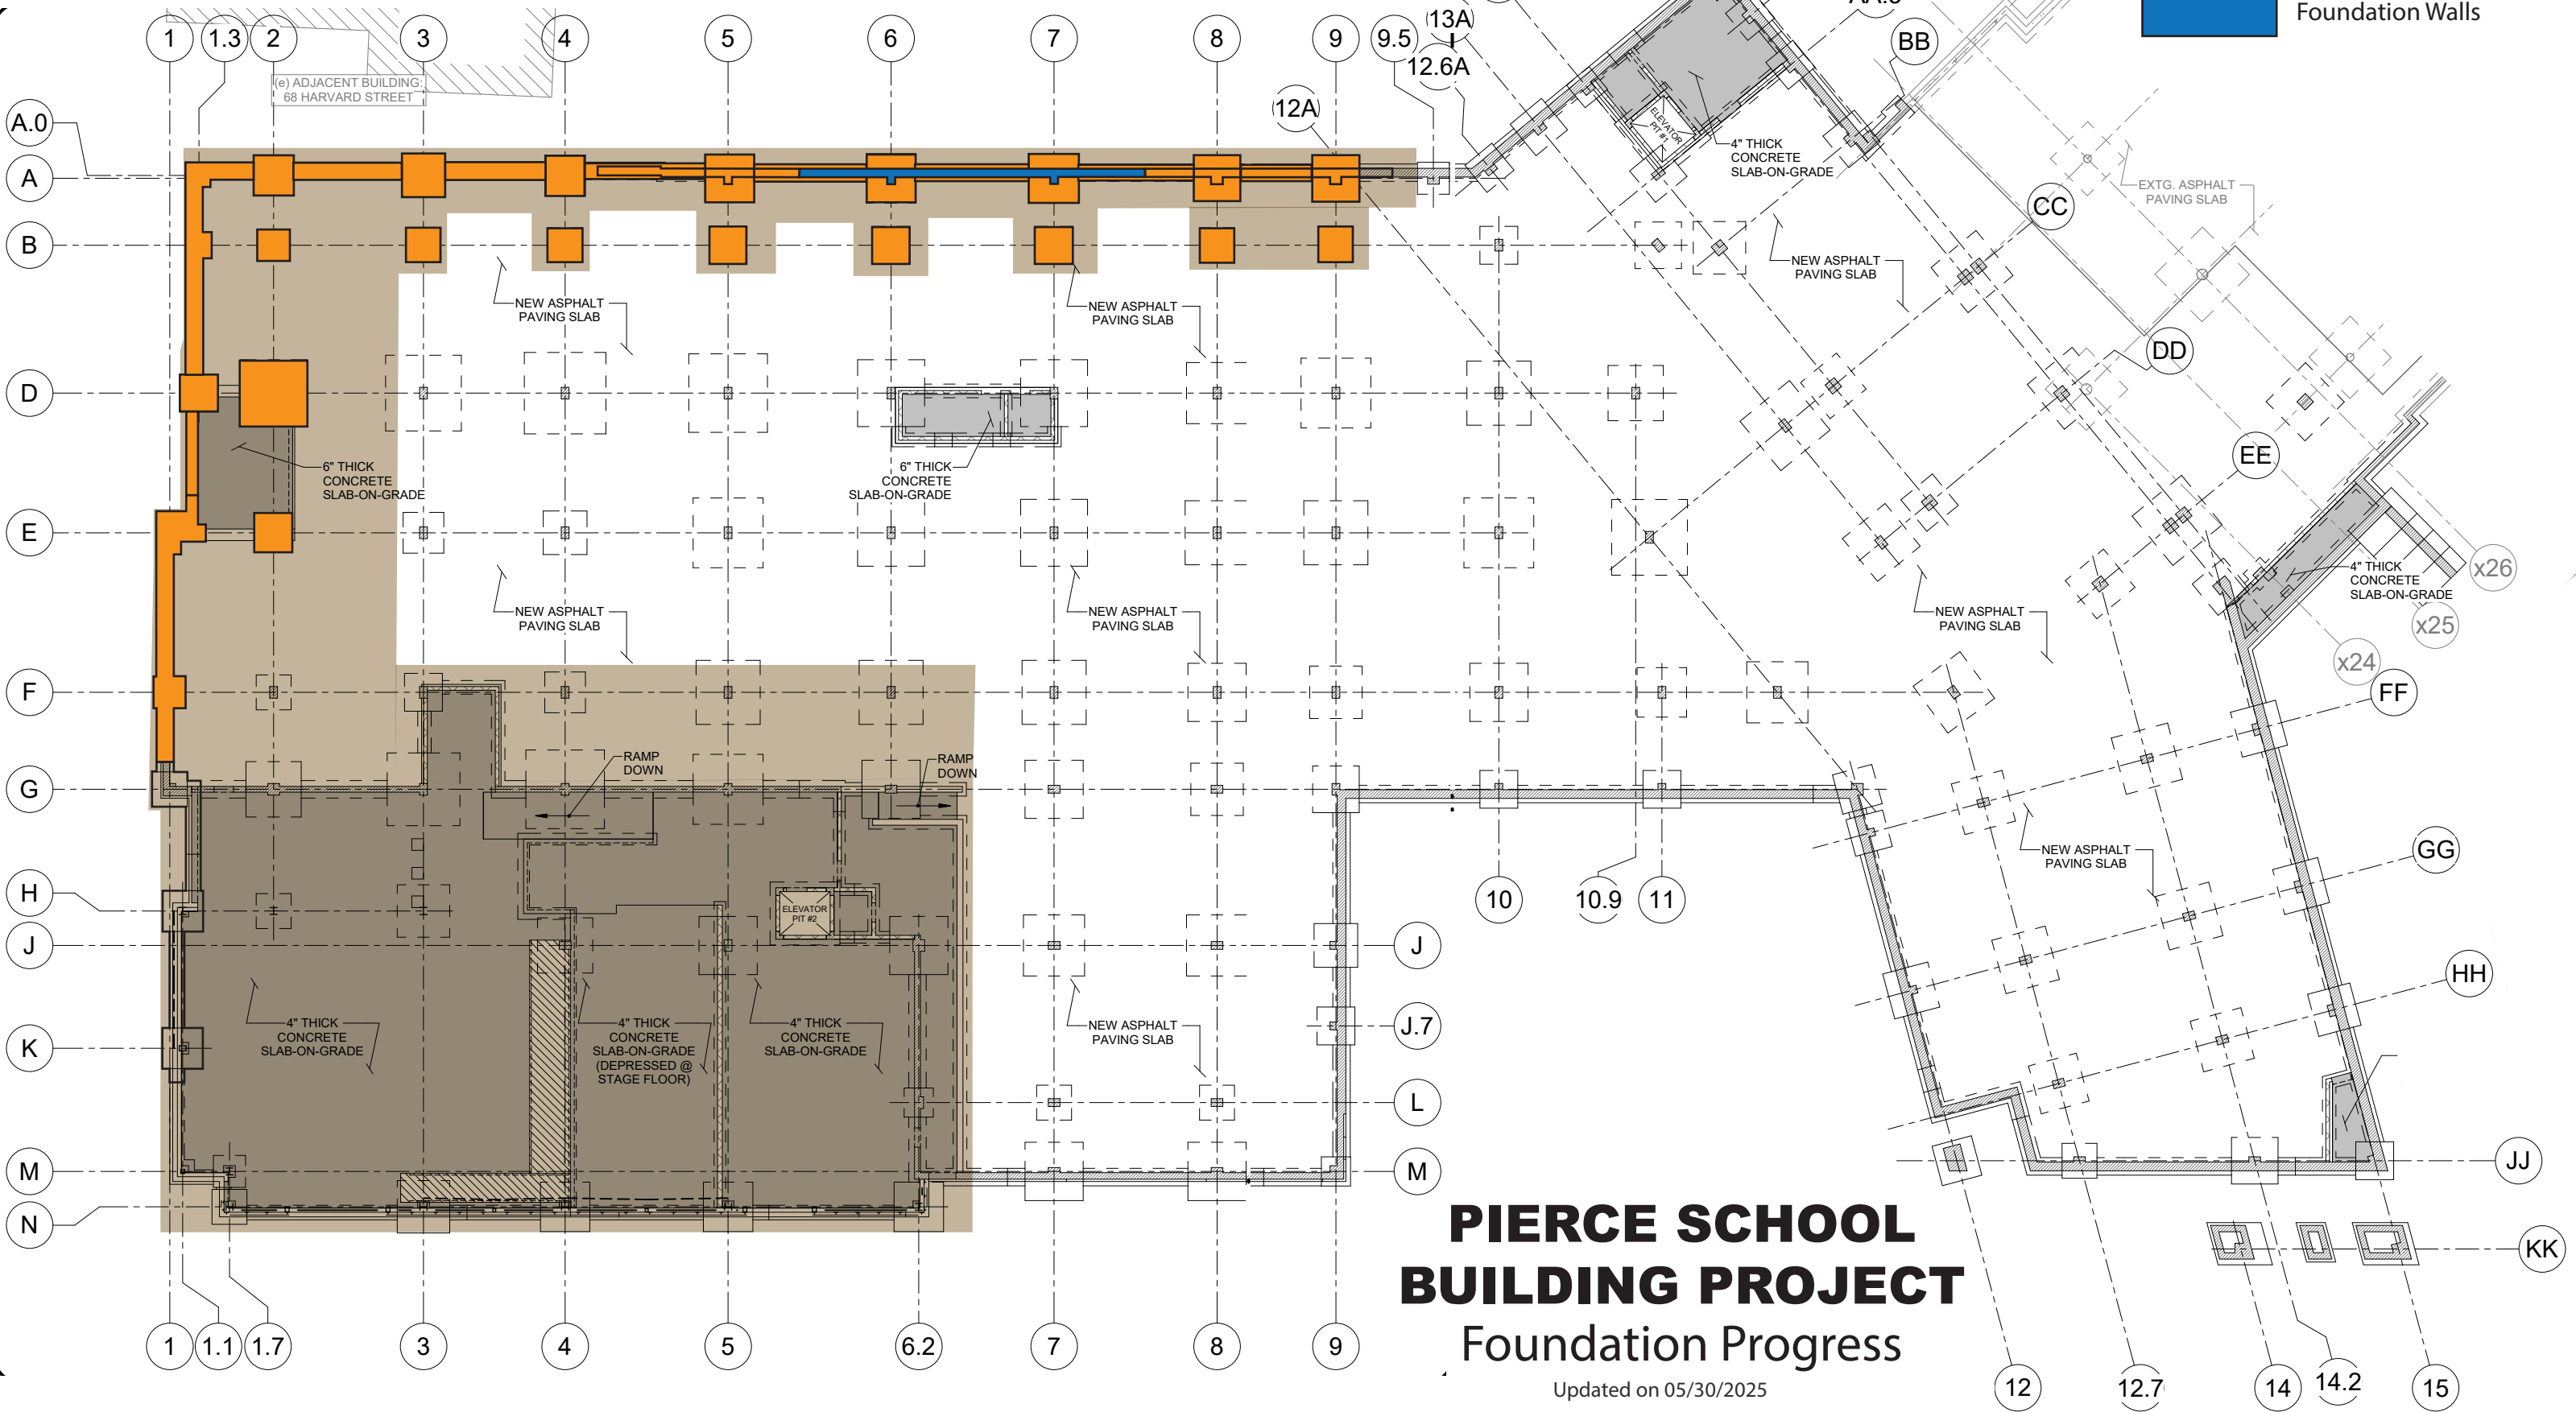

**PIERCE SCHOOL
BUILDING PROJECT**
Foundation Progress

Updated on 05/30/2025
