


DRISCOLL SCHOOL WEEKLY UPDATE

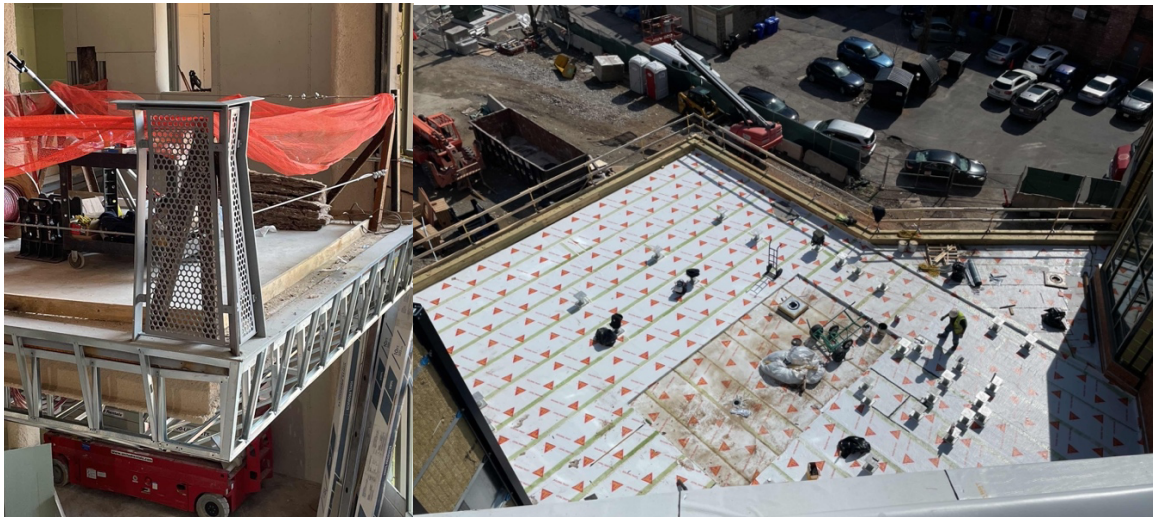

THIS WEEK'S PROGRESS

(March 13 – March 18)

- Brick finished on the West side of Area B.
- Glazing continued, North side of Area B.
- The installation of metal panels, girts and insulation continued at Area A/B South.
- Drywall installation was ongoing in Area B.
- Painting continued in Areas A and C floors 2-4.
- Ceiling grid was installed in Areas A, C.
- Electrical work continued in B, main electric room and electric closets in A and C.
- Ductwork was ongoing in Area B levels 2 and 3, Area A basement.
- The generator was placed in its final location.
- The Pre-K playground work was ongoing.
- The walk-in cooler was delivered.
- **Work is scheduled for Saturday 03/18/22.**

PROJECT TRACKING:

Area C ceilings: 60%
Area B drywall: 95%
Area B masonry: 98%

ANTICIPATING NEXT WEEK

(March 20 – March 25)

- Glass installation will finish on B North.
- Exterior metal panels will be ongoing.
- Masonry will continue on the balance of B South.
- Interior taping, sanding and painting will continue in Areas C and A, levels 2,3,4 and drywall will continue in Area B levels 1-4.
- Ceiling install will accelerate in Areas C and A.
- Roofing will continue on the Pre-K playground
- Roof coping work will begin.
- **Work is planned for Saturday 03/25/23.**

MILESTONE DATES:

- Area B drywall complete, 03/29/23
- Building tight: 03/10/23 03/24/23
- Certificate of Occupancy: 09/15/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
