




# LEFTFIELD

## DRISCOLL SCHOOL WEEKLY UPDATE

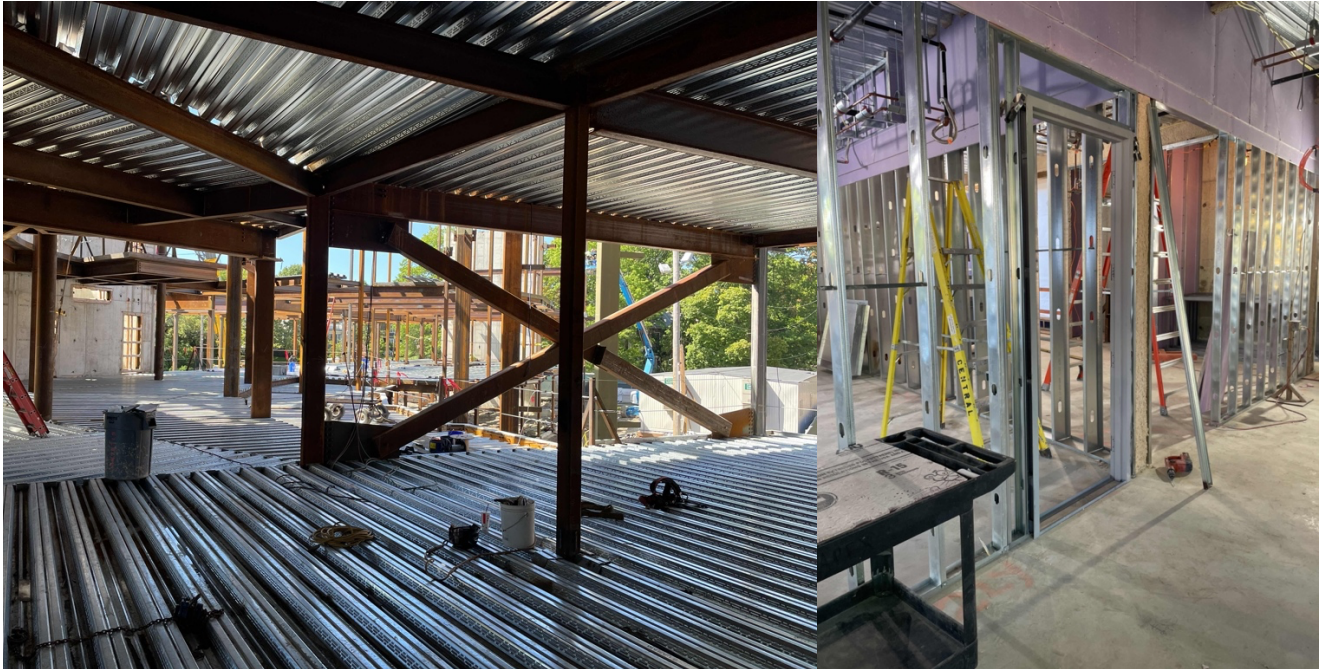

### THIS WEEK'S PROGRESS

(September 6 – September 9)

- Brick installation was ongoing at the West and North elevations of Area C.
- Interior wall framing in Area A is progressing on levels 1-3.
- Exterior framing in Area A is ongoing at South, North and East elevations
- Fire protection, plumbing and mechanical piping continued in Area A, all levels.
- Steel erection and decking is ongoing in Area B with steel up to level 4.
- No work is anticipated for Saturday 9/10/22.

### PROJECT TRACKING:

Area C Exterior framing/sheathing: 100%

Area A concrete slab on deck: 100%

Overall Steel completion: 91%

### ANTICIPATING NEXT WEEK

(September 13 – September 16)

- Steel erection and decking will continue in Area B, up to the roof.
- Interior framing and sheathing will be ongoing in Area A, levels 2-4.
- The masons will continue with brick on the West and North elevations of Area C.
- Roof edge work will begin in Area A.
- MEP trades will continue their work in Area A to include levels 3 and 4.
- No work is currently scheduled for Saturday 9/17/22

### MILESTONE DATES:

- Structural Steel complete: 9/16/22
- Concrete slabs complete: 10/10/22
- Building tight: 01/26/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
