




THE RIGHT CHOICE IN PROJECT MANAGEMENT

DRISCOLL SCHOOL WEEKLY UPDATE

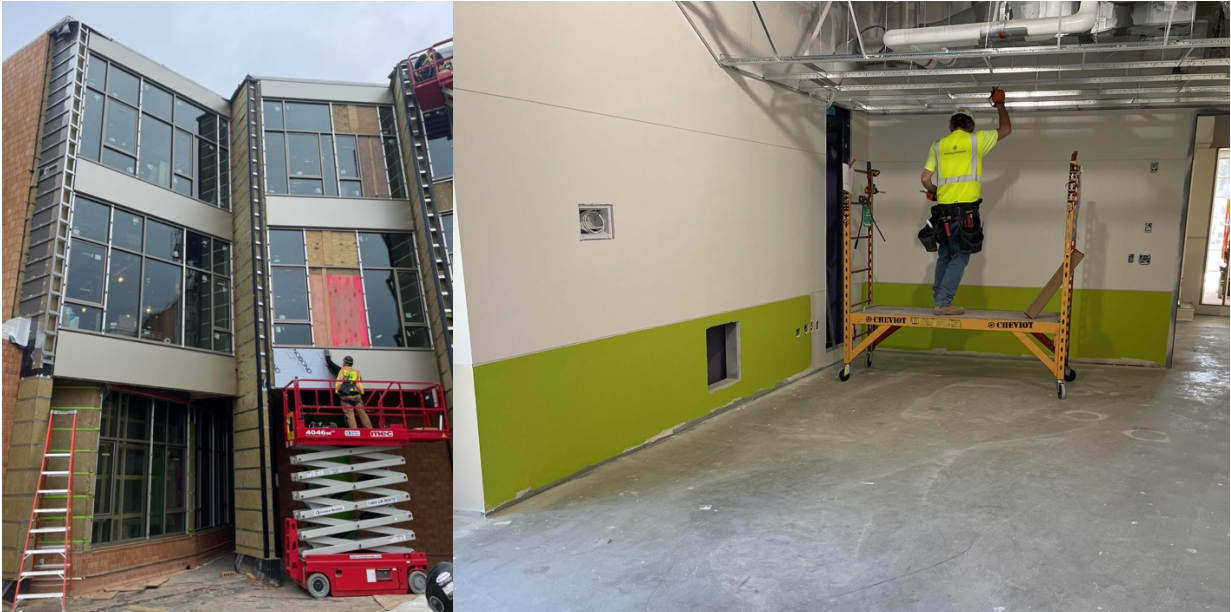

THIS WEEK'S PROGRESS

(February 6 – 10)

- Brick continued on the North side of Area B.
- The low roof at Area B4 South was completed.
- Window frame and glass installation was ongoing at South Area A and B.
- Metal panel installation began at Area A North.
- Drywall installation continued in Areas A and finished in Area C.
- Painting continued in Area C floors 2, 3 and 4.
- Ceiling grid was being installed in Area C.
- Electrical overhead and rough was ongoing in B.
- Ductwork ongoing in Area A level 4 and finished in core AB.
- **Work is scheduled for Saturday 02/11/22.**

PROJECT TRACKING:

Area C ceilings: 40%
Area A drywall: 85%
Area B masonry: 90%

ANTICIPATING NEXT WEEK

(February 13 – 17)

- Glass installation will continue at Area B South elevation and at the West Terrace.
- Exterior metal panels will be installed.
- Masonry will finish on Area B North and begin on the West (and final) side of the building.
- Interior drywall, taping and sanding will continue in Areas C and A, levels 2, 3 and 4 and drywall will continue in Area B levels 1 and 2.
- Painting will continue in Areas C and A.
- Ceiling installation will continue in Area C.
- Plumbing in basement will be inspected.
- **Work is planned for Saturday 02/18/23.**

MILESTONE DATES:

- Area A drywall complete, 02/24/23
- Area B drywall complete, 03/29/23
- Building tight: 03/08/23
- Certificate of Occupancy: 09/15/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
