


## DRISCOLL SCHOOL WEEKLY UPDATE

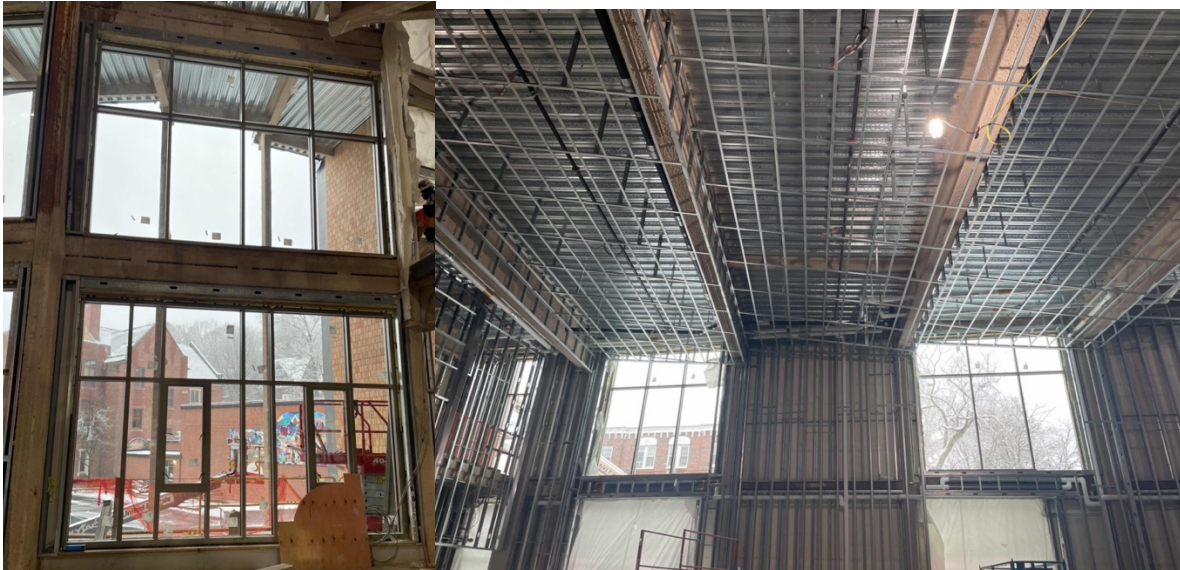

### THIS WEEK'S PROGRESS

(February 27 – March 4)

- Brick continued on the West side of Area B.
- Window frame and glass installation was ongoing at South Area A/B and the terrace.
- Metal panel installation continued at Area A North, Area C West, North and East.
- Drywall installation finished in Area A.
- Painting continued in Areas A and C floors 2-4.
- Ceiling grid was installed in Areas A, C.
- Electrical overhead and rough continued in B.
- Ductwork was ongoing in Area A levels B, 4 and in Area B level 1, hangers in B2/B3.
- Treads and risers for Stair #4 were installed.
- **Work is scheduled for Saturday 03/04/22.**

### PROJECT TRACKING:

Area C ceilings: 40%  
Area B drywall: 45%  
Area B masonry: 94%

### ANTICIPATING NEXT WEEK

(March 6 – March 11)

- Window sill installation will start on B North.
- Exterior metal panels will be ongoing.
- Masonry will continue on the West side of the building.
- Interior drywall, taping and sanding will continue in Areas C and A, levels 3 and 4 and drywall will continue in Area B levels 1-4.
- Painting will continue in Areas C and A.
- Ceiling install will continue in Areas C and A.
- Posts for playground equipment on the Pre-K roof will be installed.
- **Work is planned for Saturday 03/11/23.**

### MILESTONE DATES:

- Area B drywall complete, 03/29/23
- Building tight: 03/08/23
- Certificate of Occupancy: 09/15/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
