




THE RIGHT CHOICE IN PROJECT MANAGEMENT

DRISCOLL SCHOOL WEEKLY UPDATE

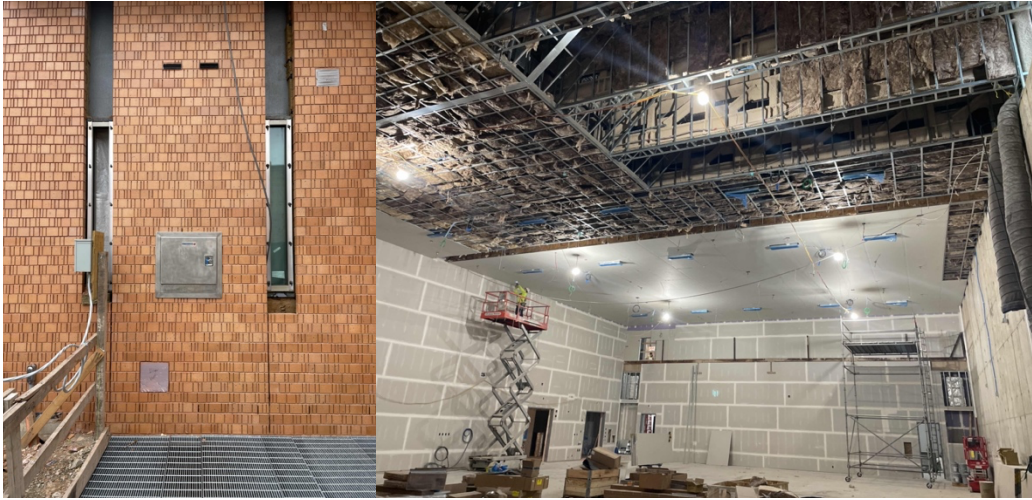

THIS WEEK'S PROGRESS

(April 3 – April 8)

- Misc. brick infill around building.
- The installation of girts and insulation continued at Area A/B South and B North.
- Trespa panel installation continued at Area C East, West and North.
- Drywall installation was ongoing in Area B.
- Painting continued in Areas A and C floors B-4.
- Ceiling grid was installed in Areas A, C.
- Electrical work continued in B, main electric room, the generator and lights in Areas C, A.
- Ductwork was ongoing in Area B levels 3 and 4, Area A and C basement.
- **Permanent power was turned on.**
- The Pre-K playground roofing was ongoing.
- Millwork installation continued in Areas A and C levels 2, 3.
- **Work is scheduled for Saturday 04/08/22.**

PROJECT TRACKING:

Area C ceilings: 90%
Area B paint: 15%
Area A ceilings: 65%

ANTICIPATING NEXT WEEK

(April 10 – April 15)

- Curtainwall installation will continue.
- Masonry will continue in leave-out areas and other minor infill.
- Interior taping, sanding and painting will continue in Areas C and A, levels 2,3,4 and drywall will continue in Area B levels 1-4.
- Ceiling install will continue in Areas C and A.
- Light fixtures will be installed in Areas C and A.
- Roofing will continue on the Pre-K playground
- Roof coping work will continue.
- Millwork will continue in Areas C and A.
- Elevator installation will continue.
- Sitework will re-start on the Westbourne Terrace side of the site.
- **Work is planned for Saturday 04/15/23.**

MILESTONE DATES:

- Millwork complete: 06/27/23
- Terrazzo complete: 06/28/23
- Certificate of Occupancy: 09/15/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
