


LEFTFIELD

DRISCOLL SCHOOL WEEKLY UPDATE

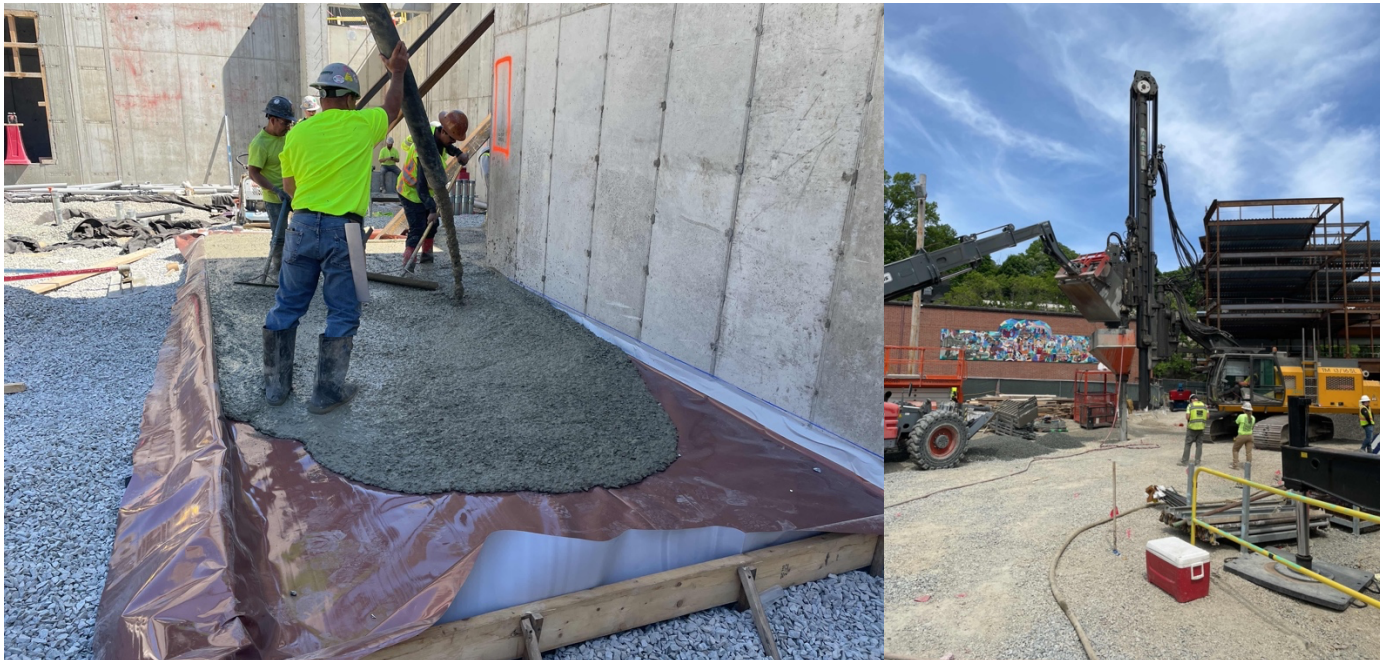

THIS WEEK'S PROGRESS

(May 23 – May 27)

- Core AB 4th level walls were poured
- Waterproofing, backfilling and compaction continued around the building.
- Underground electrical and plumbing work was ongoing, with a partial plumbing inspection achieved.
- Geopier installation was ongoing on the East side of the site.
- The 2nd floor slab at Building C was poured.
- **No work is planned for Saturday 5/28/22.**

PROJECT TRACKING:

Area C concrete slabs: 34%

Area C steel: 95%

ANTICIPATING NEXT WEEK

(May 31 – June 3)

- The 5th level walls of Core AB will be formed.
- Geopier work will finish this week.
- Underground electrical and plumbing work will continue.
- Concrete slabs in Area C on floors 3 and 4 will be poured.
- Footings along Washington St. will be formed.
- **No work is scheduled for Monday 5/30/22**

MILESTONE DATES:

- Structural Steel begins: 3/28/22
- Foundations complete: 6/21/22
- Structural Steel complete: 8/30/22

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
