




THE RIGHT CHOICE IN PROJECT MANAGEMENT

## DRISCOLL SCHOOL WEEKLY UPDATE

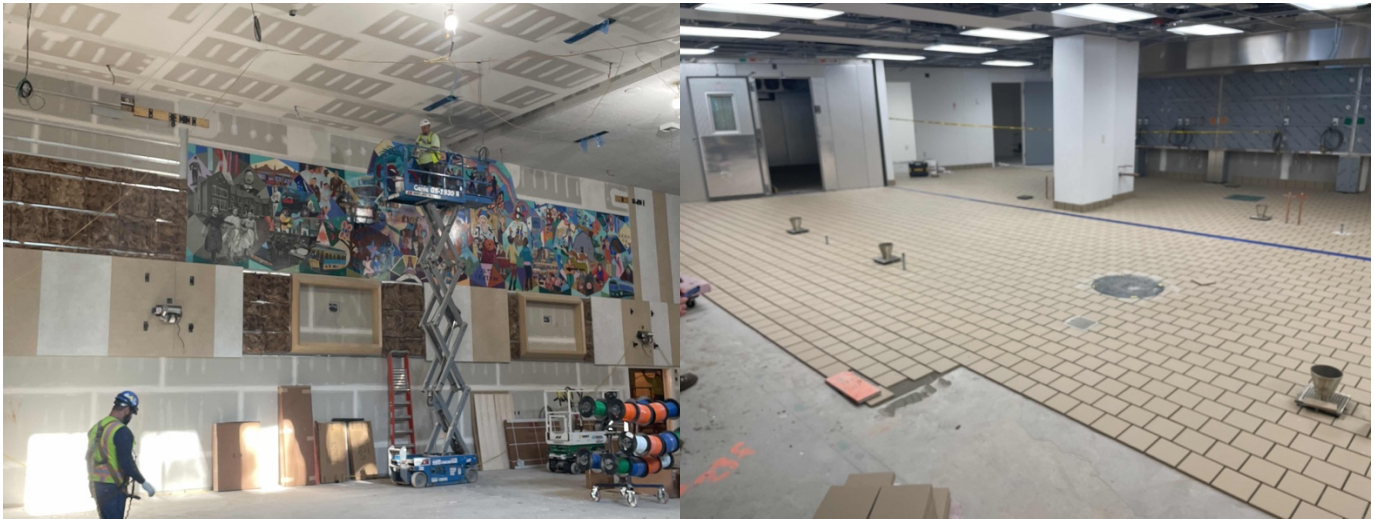

### THIS WEEK'S PROGRESS

(May 22 – May 27)

- Trespa panel installation continued at Areas A, C and B.
- Painting continued in Areas A, B and C.
- Ceiling grid and tile continued in all Areas.
- Quarry tile was installed in the kitchen.
- Exterior and interior doors were hung.
- Electrical work continued in all areas.
- Ductwork was ongoing in B4 and A0.
- Millwork installation continued in Areas A, C and B, levels 2, 3 and 4.
- The elevator installation was ongoing.
- Roof edge trim work re-started.
- VCT work started in Area A level 3.
- Pipe for the temp cooling system was installed.
- Forms, rebar and concrete continued for the North Ramp adjacent to Westbourne Terrace.
- **No work is scheduled for Saturday 05/27/22.**

### PROJECT TRACKING:

Area C: millwork: 75% complete

Area B: paint: 95%, millwork 5%

Area A: ceilings/paint 95%, millwork 60%

### ANTICIPATING NEXT WEEK

(May 29 – June 3)

- Exterior soffits will continue.
- Painting will continue in the Multipurpose Rm.
- Ceiling grid and tile installation will continue.
- Interior glazing and frames will continue.
- Tel/data wiring will continue, and lights will be installed in Areas C, A and B.
- Millwork installation will continue in all areas.
- VCT, ceramic and quarry tile work will continue.
- The elevator installation will continue.
- The hydrant on Washington St will be completed.
- The North Ramp foundation work will continue.
- **A portion of the Westbourne sidewalk at the site will remain closed for sitework.**
- **Work is planned for Saturday June 3<sup>rd</sup>.**

### MILESTONE DATES:

- Elevator installed: 06/08/23
- Millwork complete: 06/27/23
- Terrazzo complete: 06/28/23
- Certificate of Occupancy: 09/15/23

For Traffic Safety Enhancements and other project details, please visit the Project Website:

<https://www.brookline.k12.ma.us/Page/2353>
