

PIERCE SCHOOL WEEKLY UPDATE, 10/31/25



THIS WEEK (October 27-31)

- Concrete pour #5 (structural deck)
- Steel erection, metal deck ongoing, Bldg A
- Rebar, MEP sleeves on struct. deck
- Perimeter drain/backfill at A line ongoing
- Plumbing trenches in Historic Building ongoing
- Sewer work in Pierce Street ongoing

PROJECT TRACKING:

- Structural steel: 65%

ANTICIPATING NEXT WEEK (November 3-7)

- Steel erection and metal deck ongoing
- Concrete pours 6 and 7 in Bldg B.
- Drill and dowel rebar at Hist. Bldg. foundation
- Continue sewer work in Pierce Street
- Begin MEP underground work in Bldg. A
- Performance testing of the building mock-up

MILESTONES:

- Deck pours #5, 6, 7: 10/31, 11/4, 11/6
- Steel erection Bldg A Phase 1: 11/04/25

Narrative:

Concrete pour #5 at the structural deck of Building B was completed early, on 10/31. Rebar and MEP work for the next pours are also ahead of schedule for next week.

Steel erection continues to make very good progress in Building A; welds and bolts were tested this week. Metal deck continues to be installed/spread as the crews erect steel. Building A erection should finish next week, with a couple of weeks of detailing to follow. The utility crew on Pierce Street continued their work on the sewer line. The site contractor continued with perimeter drainage and backfilling along A line.

The electricians have been working on temp lighting and wiring in Building A as well as sleeves and conduit on the deck. Plumbers have been doing layout and installing sleeves on the structural deck.

Excavation for plumbing in the Historic Building basement was ongoing.


Overall, the project remains on schedule.


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



Bldg A Bldg B

-  Footing/Site Prep
-  Footings
-  Foundation Walls
-  Structural Slab

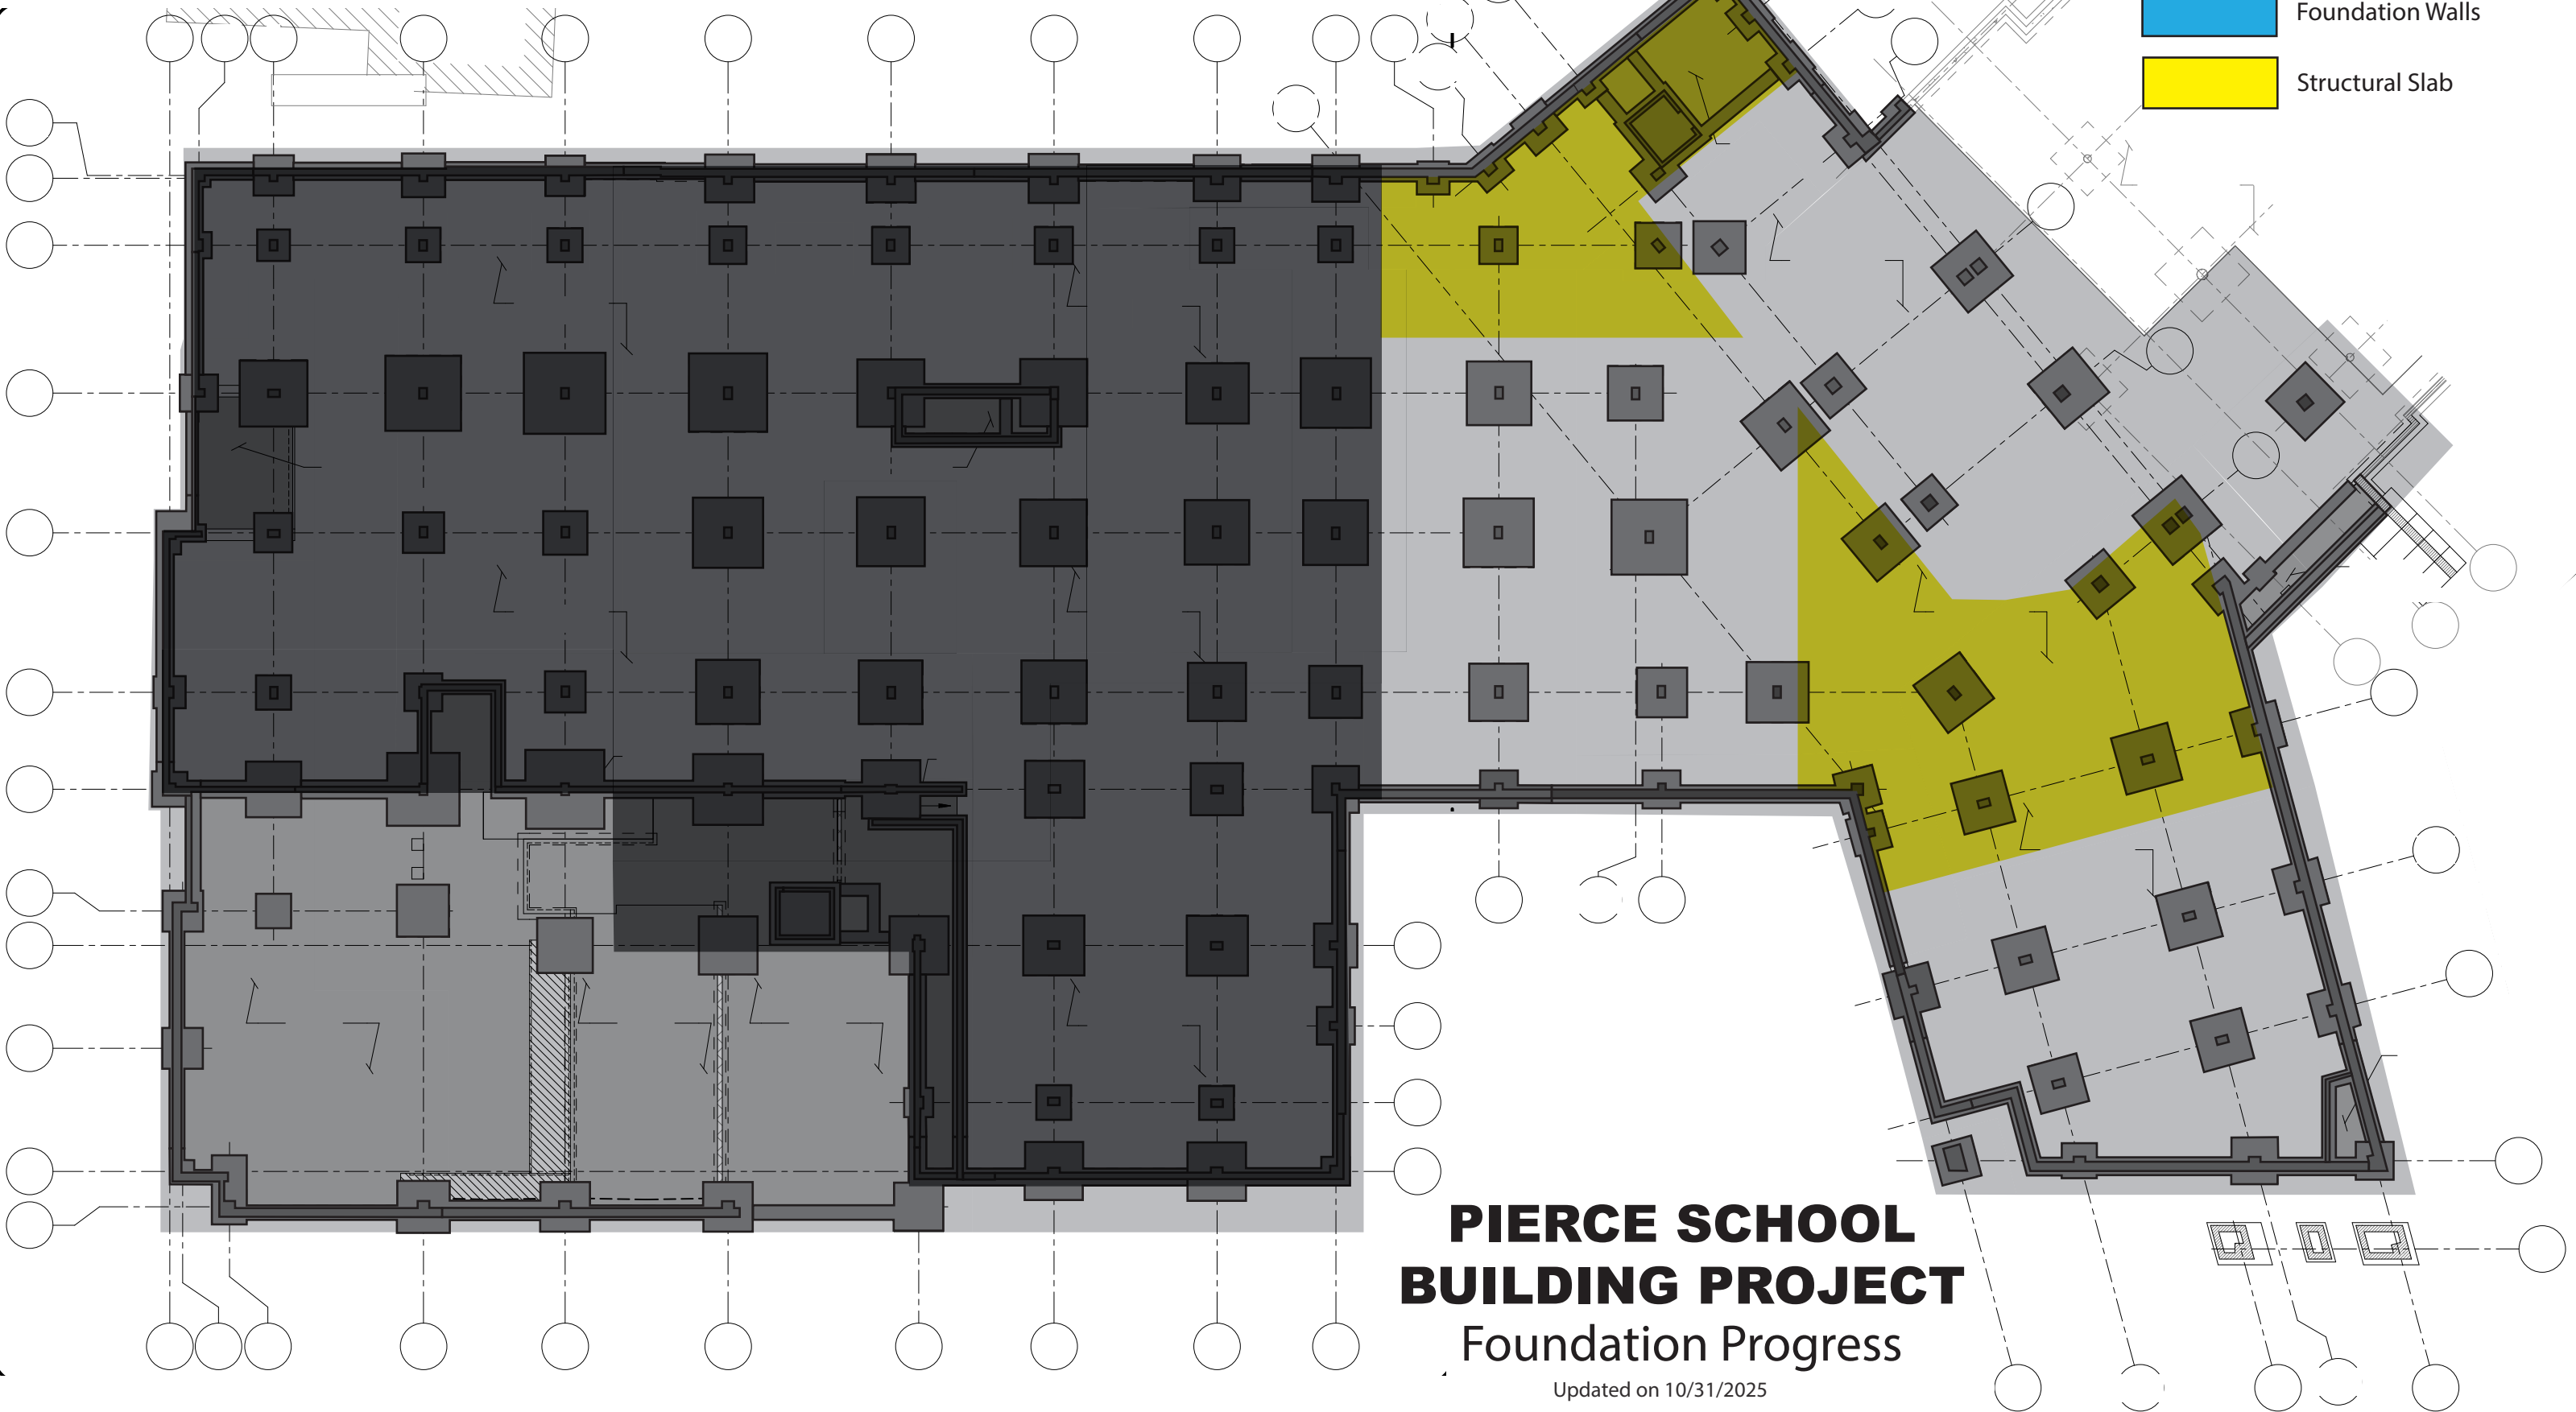

**PIERCE SCHOOL
BUILDING PROJECT**
Foundation Progress

Updated on 10/31/2025
