

WHAT: The creation of a geothermal well system for the Pierce School Project.

WHEN: November 17, 2025 through November 2026

This work has a 12 month window from start to finish, per order of the Massachusetts State Legislature and the Article 97 process.

Typical construction hours are 7:00am-3:30pm, Monday through Friday. Work on Saturdays (as needed) is 8:30am - 5:00pm.


HOW:	
Perimeter construction fence/mobilization/signs/protection	Nov/Dec 2025
Strip topsoil/clear site	Jan 2025
Drill wells (80 wells @ 600' deep)	Jan-March 2026
Excavate for/install/test/backfill well circuit piping	April-May 2026
Backfill and restore ballfield	July-Aug 2026
Pave sidewalks	August 2026
Seed grass areas	Sept 2026
Install plantings	Oct 2026
Punch list/remove all construction items - work complete	Nov 2026

- You will hear:**
- Truck backup alarms.
 - Heavy equipment (excavators, loaders) in operation, similar to the equipment used for the new Pierce School.
 - Drilling rigs.
 - Generators running.
- NOTE: Sound levels will be monitored daily during drilling.

- You will see:**
- Construction fencing and signs, redirecting pedestrians around the work
 - Trucks and equipment entering and exiting the site from the School Street parking lot.
 - Construction equipment staged on the basketball courts
 - Temporary work lights

CONTACT:

For Parks and Open Space questions/comments:
parks@brooklinema.gov
For construction-related issues:
Andrew Deschenes, LeftField Project Management
adeschenes@leftfieldpdm.com

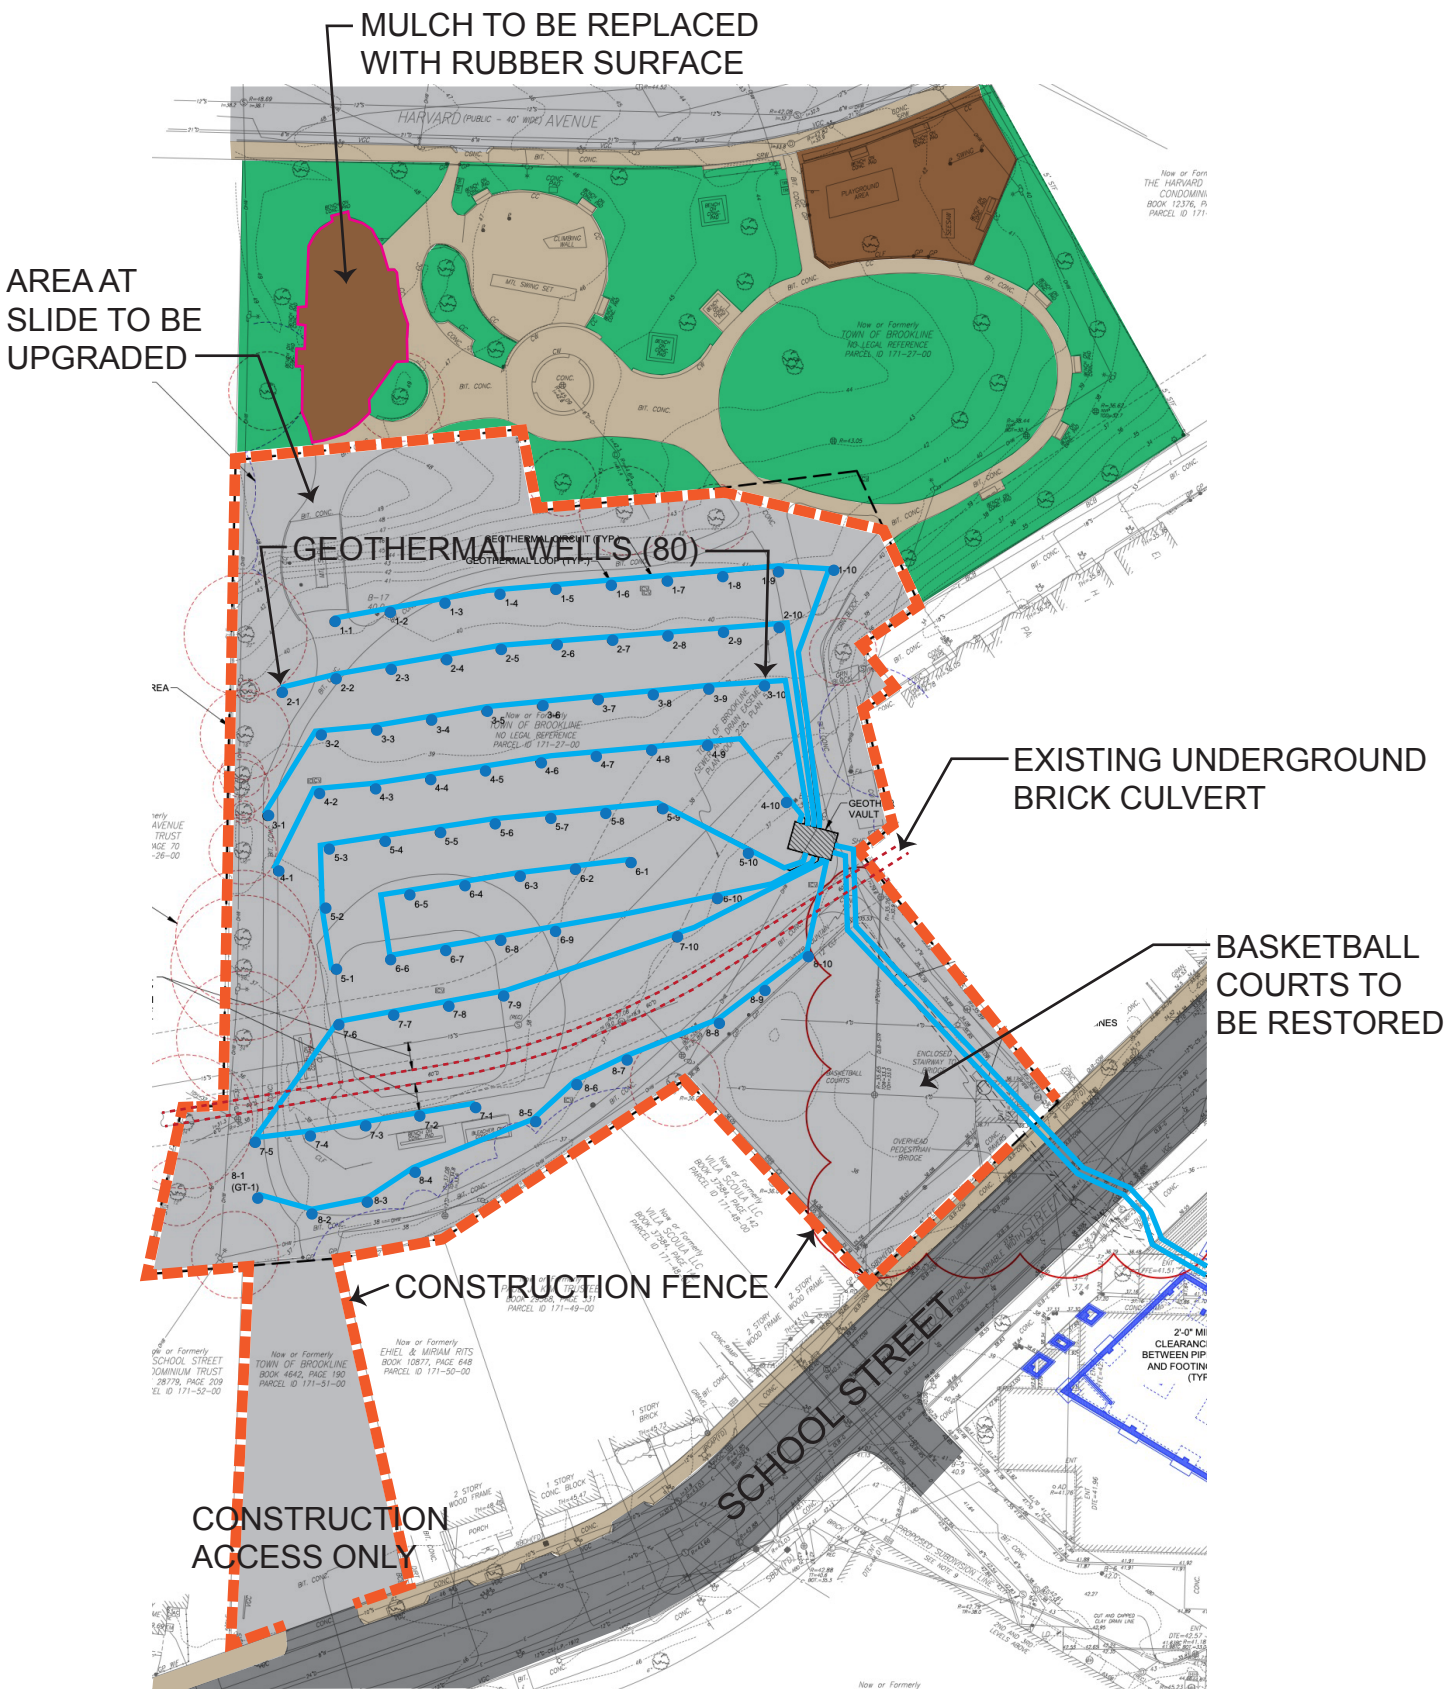

For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>
To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>
