



THE RIGHT CHOICE IN PROJECT MANAGEMENT

# PIERCE SCHOOL WEEKLY UPDATE



**NOTE: Demolition is paused while the demo debris is processed, sorted and trucked out.**

## THIS WEEK (January 20-24)

- Processed and sorted concrete/metal debris
- Trucked out materials
- Began drilling for piles for Support of Excavation (SOE) work

## PROJECT TRACKING:

- Building Demolition 80% complete

## ANTICIPATING NEXT WEEK (January 27-31)

- Process, sort and truck out material
- Drill/install piles for SOE

## MILESTONES:

- Support Of Excavation (SOE) begins: 01/20/25
- Above grade demo complete: 01/31/25

For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>


To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



# PIERCE SCHOOL BUILDING PROJECT

## Demolition Progress as of 01/24/25

Please note:  
There is a pause in demolishing the remaining building while the demolition debris is processed, sorted, and trucked out to make room for the remaining work.

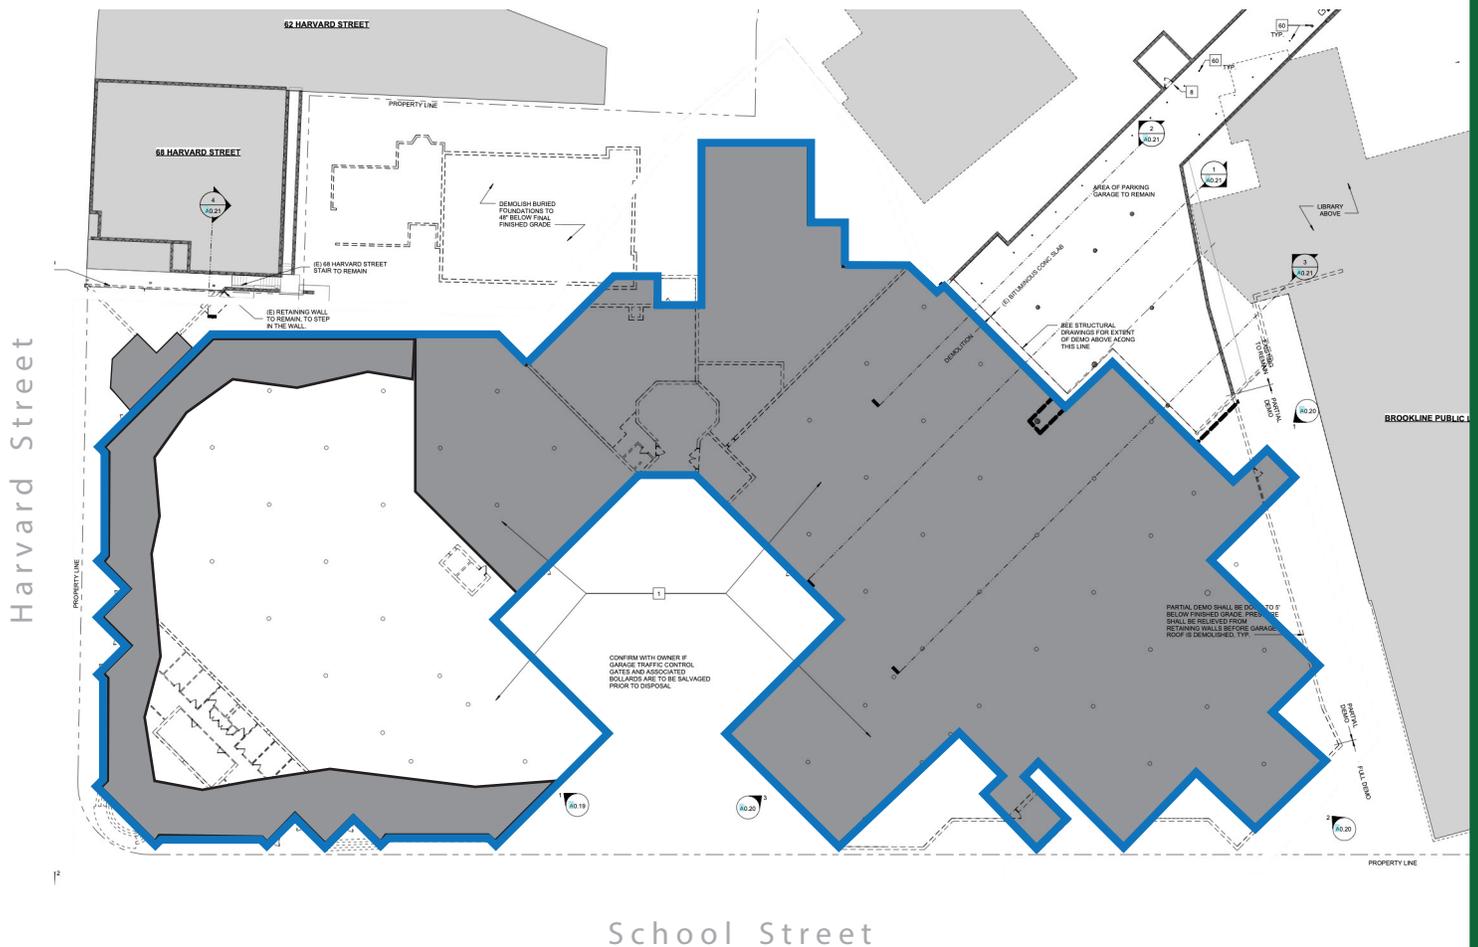

- Demolition this week
- Completed demolition
