


## **Edward Devotion School**

School Building Committee Meeting
September 25, 2017

## HM FH HMFH ARCHITECTS

















A building mockup panel was constructed to demonstrate aesthetic effects, qualities of materials, execution and review of construction workmanship. Proceeding approval, brick masonry work began at the southern facing façade of the school.



























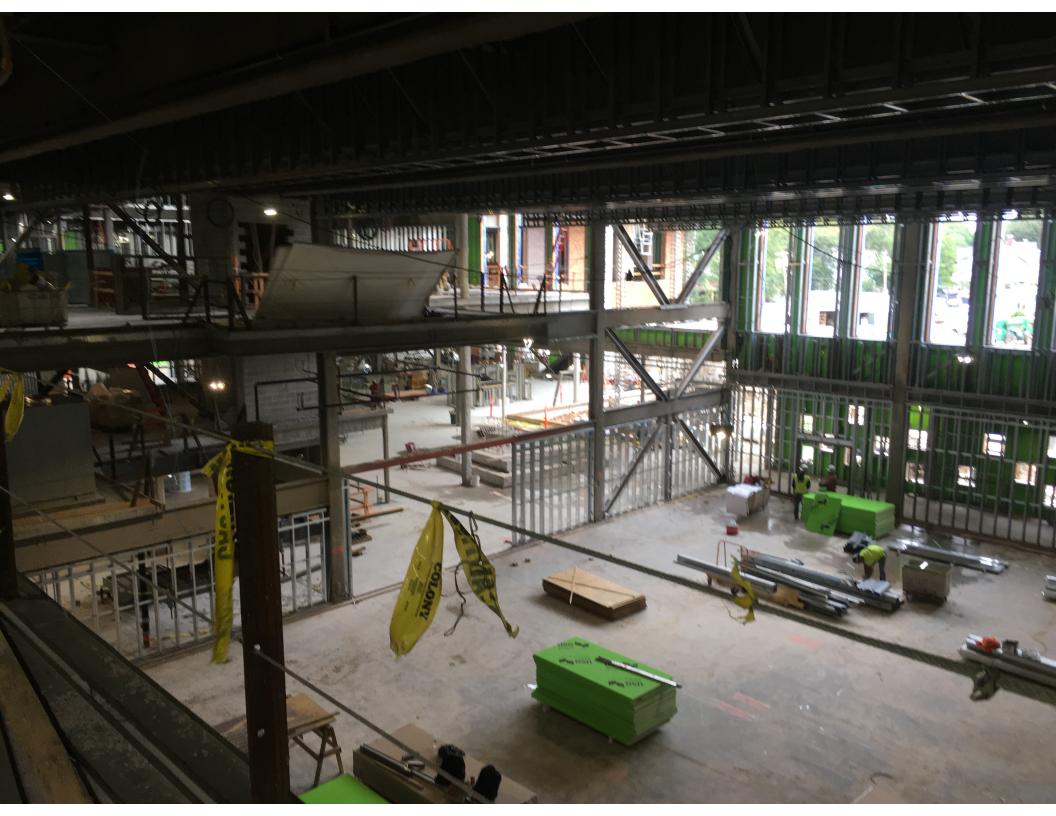

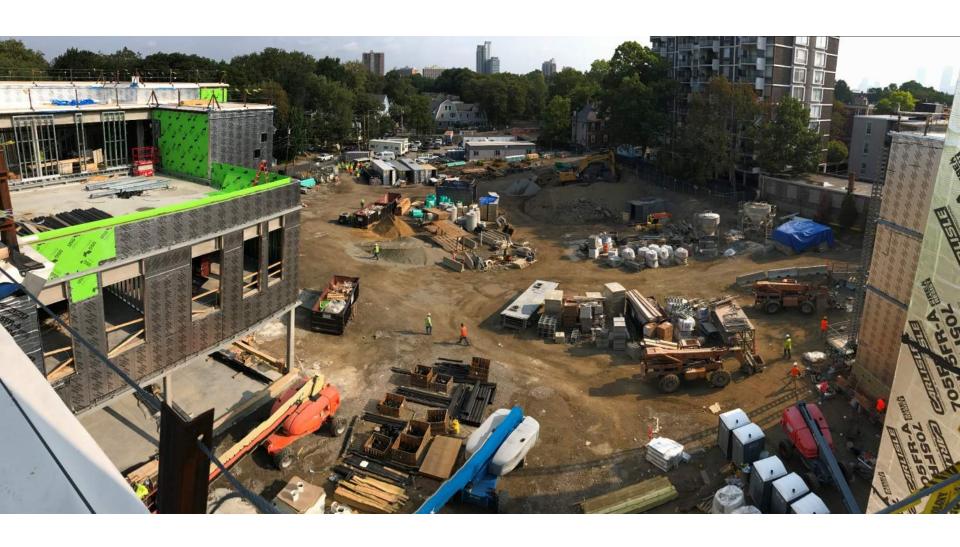



## Edward Devotion School Project Schedule Summary 9/25/17

	October				Т	November			ī	December			January 2018			February			March	April			Мау			June			I	July			August			
Air-Vapor Barrier																																				
Exterior Masonry																																				
Curtainwall / Windows																																				
MEP Rough-in																																				
Interior Frame/Drywall																																				
Casework/Millwork																																				
Interior finishes																																				
MEP Commisioning																																				
Site / Landscape																																				
FF&E, Move-in																																				
De-Mobilization																																				

