Driscoll School - Gantt Project Report

Plans: All Plans Selected

Roles: All Roles Selected

Locations: Multiple Locations Selected (Including Location-less tickets)

Start Date: Wednesday January 26 2022

End Date: Thursday February 17 2022

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role
Ready for Steel	378		2021-06-12	2022-06-24			
Core C 34-45 (2nd Flr to 3rd Flr)	9	10	2022-01-20	2022-02-01			Concrete Marguerite
CY from C14 to core C	6	10	2022-01-21	2022-01-28			Concrete Marguerite
FRP Footing & Starter Walls @ Colum n Line A2 to AM.6	6	9	2022-01-21	2022-01-28			Concrete Marguerite
Contract, Design, Approval of Wall Su pport Systetm	15	1	2022-01-24	2022-02-11			GC - Gilbane
Foundation walls A1 to A15	5	9	2022-01-24	2022-01-28			Concrete Marguerite
Response to RFI 019.1 & Design of Wall Support			2022-01-26	2022-01-26	2022-01-26	2022-01-26	GC - Gilbane
Geo Pier Submittals			2022-01-28	2022-01-28			GC - Gilbane
Foundation walls c21.6 from core C t o approximately CQ	7	10	2022-01-31	2022-02-08			Concrete Marguerite
Hold for waterproofing	1	2	2022-01-31	2022-01-31			Armani Waterproofing
Excavate for Underground and Backfil l for slab on grade placement at eleva tor hallway	9	4	2022-01-31	2022-02-10			Derenzo
Assemble Climbing System	1	10	2022-02-02	2022-02-02			Concrete Marguerite
Hold for waterproofing	5	2	2022-02-02	2022-02-08			Armani Waterproofing
Core C 45- 58	5	10	2022-02-03	2022-02-09			Concrete Marguerite
UG Plumbing A1-AM.6	2	2	2022-02-08	2022-02-09			PJ Kennedy UG Plumbing
Foundation walls along C21.6 From C Q to approximately CG Form , rebar , place , strip.	7	10	2022-02-09	2022-02-17			Concrete Marguerite
UG Electrical	2	2	2022-02-09	2022-02-10			Griffin Electrical
Assemble Climbing System	1	10	2022-02-10	2022-02-10			Concrete Marguerite
Core C 58-71	5	10	2022-02-11	2022-02-17			Concrete Marguerite

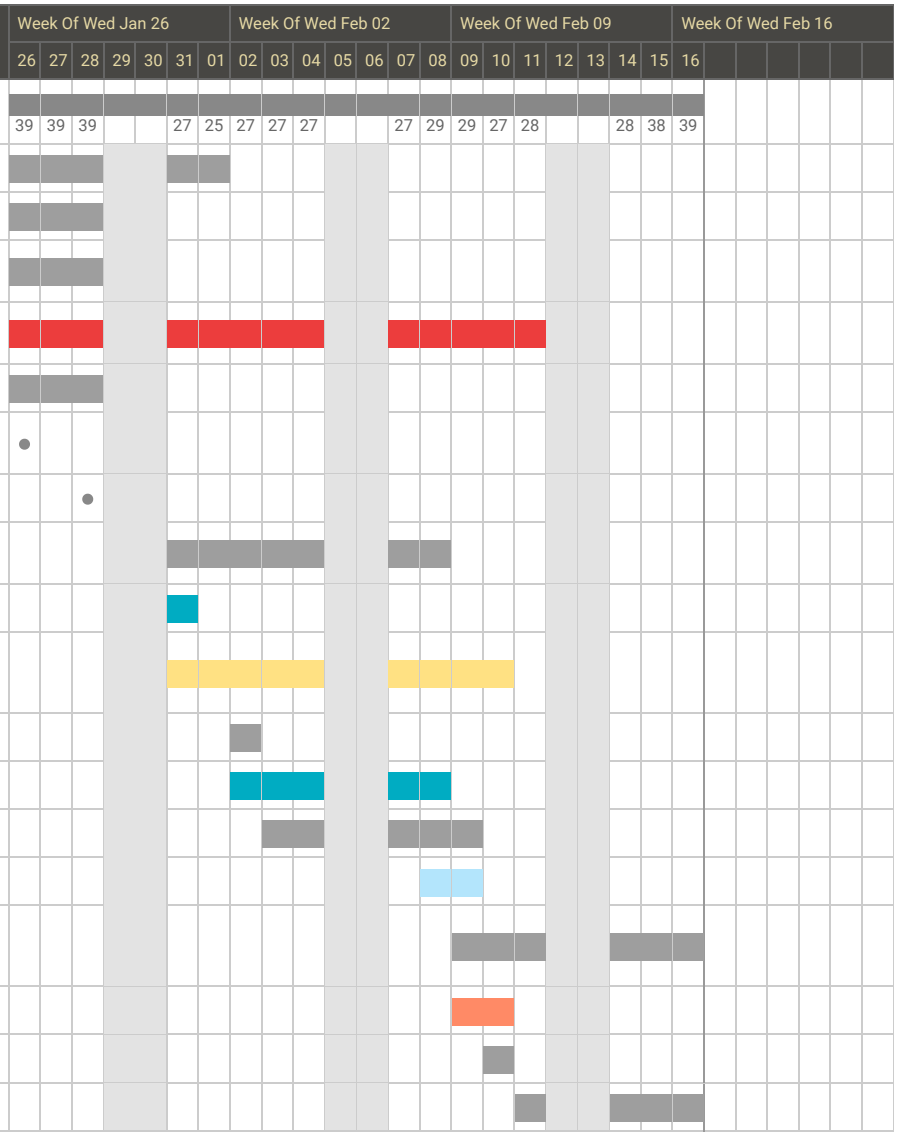

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role
Hold for waterproofing	5	2	2022-02-11	2022-02-17			Armani Waterproofing
Slab on Grade at Elevator Hallway Are a	6	5	2022-02-11	2022-02-18			Concrete Marguerite
Install Wall Bracing	8	1	2022-02-14	2022-02-23			GC - Gilbane
Layout install rebar, form and place C ore A spread footing	5	10	2022-02-15	2022-02-21			Concrete Marguerite
Delivery Window for Generator	33	1	2022-02-16	2022-04-01			Griffin Electrical

Crew Size By Role	Total	Complete	Promised Incomplete	Remaining	Project Role	Week Of Wed Jan 26							Week Of Wed Feb 02							Week Of Wed Feb 09							Week Of Wed Feb 16
						26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16
All Roles	495	0 (0%)	275 (56%)	220 (44%)		39	39	39			27	25	27	27	27			27	29	29	27	28			28	38	39
	20	0 (0%)	12 (60%)	8 (40%)	Armani Waterproofing						2		2	2	2			2	2			2			2	2	2
	414	0 (0%)	214 (52%)	200 (48%)	Concrete Marguerite	38	38	38			20	20	20	20	20			20	20	20	20	25			25	35	35
	36	0 (0%)	36 (100%)	0 (0%)	Derenzo						4	4	4	4	4			4	4	4	4						
	16	0 (0%)	13 (81%)	3 (19%)	GC - Gilbane	1	1	1			1	1	1	1	1			1	1	1	1	1			1	1	1
	5	0 (0%)	0 (0%)	5 (100%)	Griffin Electrical															2	2						1
	4	0 (0%)	0 (0%)	4 (100%)	PJ Kennedy UG Plumbing														2	2							

Generated on: January 26, 2022 10:52:57 AM EST

Italic indicates a constraint.

Touchplan®
