Driscoll School - Gantt Project Report

Plans: All Plans Selected

Roles: All Roles Selected

Locations: Multiple Locations Selected (Including Location-less tickets)

Start Date: Monday January 17 2022

End Date: Tuesday February 08 2022

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role
Ready for Steel	378		2021-06-12	2022-06-24			
Core A, Footings & Walls	24		2022-01-24	2022-02-16			
Foundation walls A19 to A1	10	9	2022-01-24	2022-02-04			Concrete Marguerite
Geo Pier Submittals			2022-01-31	2022-01-31			GC - Gilbane
Foundation walls Core A to column line A19	8	9	2022-02-07	2022-02-16			Concrete Marguerite
Core C, Footings & Walls	36		2022-01-07	2022-02-11			
Begin walls CY @C4 to C14	10	10	2022-01-07	2022-01-20			Concrete Marguerite
Core C 34-45 (2nd Flr to 3rd Flr)	6	10	2022-01-20	2022-01-27			Concrete Marguerite
CY from C14 to core C	6	10	2022-01-21	2022-01-28			Concrete Marguerite
Contract, Design, Approval of Wall Support Systetm	15	1	2022-01-24	2022-02-11			GC - Gilbane
Assemble Climbing System	1	10	2022-01-28	2022-01-28			Concrete Marguerite
Core C 45- 58	5	10	2022-01-31	2022-02-04			Concrete Marguerite
Foundation walls c21.6 from core C to approximately CQ	7	10	2022-01-31	2022-02-08			Concrete Marguerite
Hold for waterproofing	5	2	2022-01-31	2022-02-04			Armani Waterproofing
Hold for waterproofing	1	2	2022-01-31	2022-01-31			Armani Waterproofing
Assemble Climbing System	1	10	2022-02-07	2022-02-07			Concrete Marguerite
Low Foundations A/B	50		2021-12-23	2022-02-10			
Sheer core A/B Mat Slab Footings and FDN Walls	21	5	2021-12-23	2022-01-20			Concrete Marguerite
Waiting for inbeds			2022-01-19	2022-01-19			GC - Gilbane
FRP Footing & Starter Walls @ Column Line A2 to AM.6	6	9	2022-01-21	2022-01-28			Concrete Marguerite

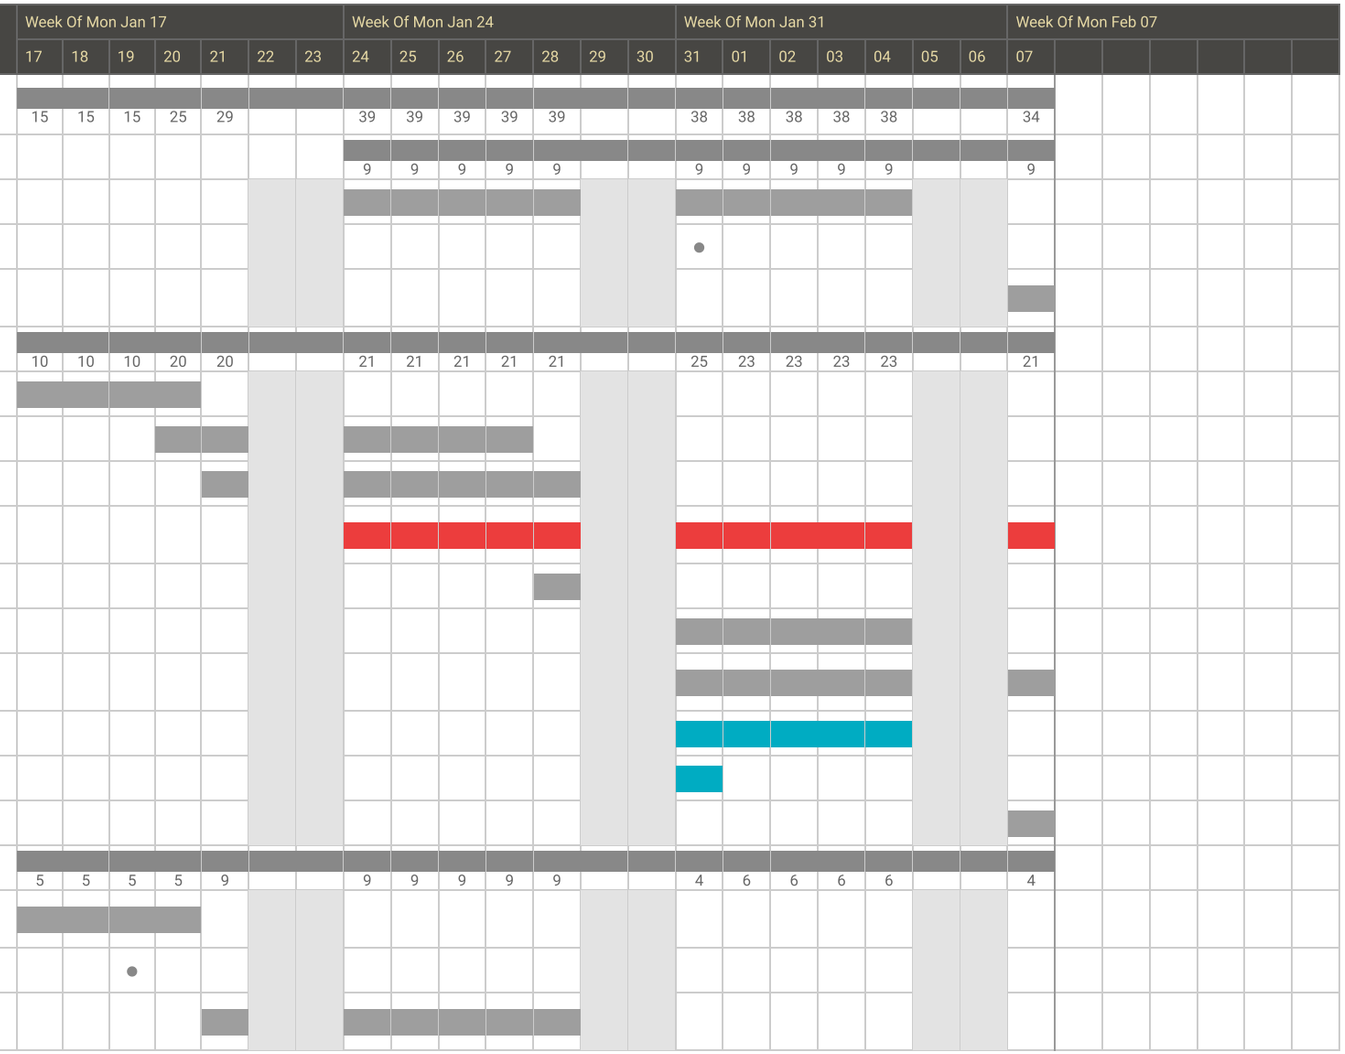

Task Description	Days	Crew Size	Planned Start	Planned Finish	Actual Start	Actual Finish	Project Role
Excavate for Underground and Backfill for slab on grade placement at elevator hallway	9	4	2022-01-31	2022-02-10			Derenzo
UG Plumbing A1-AM.6	2	2	2022-02-01	2022-02-02			PJ Kennedy UG Plumbing
UG Electrical	2	2	2022-02-03	2022-02-04			Griffin Electrical

Week Of Mon Jan 17							Week Of Mon Jan 24							Week Of Mon Jan 31							Week Of Mon Feb 07						
17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07						

Crew Size By Role	Total	Complete	Promised Incomplete	Remaining	Project Role
All Roles	518	0 (0%)	120 (23%)	398 (77%)	
	12	0 (0%)	0 (0%)	12 (100%)	Armani Waterproofing
	463	0 (0%)	120 (26%)	343 (74%)	Concrete Marguerite
	24	0 (0%)	0 (0%)	24 (100%)	Derenzo
	11	0 (0%)	0 (0%)	11 (100%)	GC - Gilbane
	4	0 (0%)	0 (0%)	4 (100%)	Griffin Electrical
	4	0 (0%)	0 (0%)	4 (100%)	PJ Kennedy UG Plumbing

Week Of Mon Jan 17							Week Of Mon Jan 24							Week Of Mon Jan 31							Week Of Mon Feb 07						
17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07						
15	15	15	25	29			39	39	39	39	39			38	38	38	38	38			34						
														4	2	2	2	2									
15	15	15	25	29			38	38	38	38	38			29	29	29	29	29			29						
														4	4	4	4	4			4						
							1	1	1	1	1			1	1	1	1	1			1						
																	2	2									
															2	2											

Generated on: January 19, 2022 01:14:56 PM EST

Italic indicates a constraint.

Touchplan®
